



**Renovate SP17 for Fleet Legal Services
RM24-3467
Naval Station Norfolk, Norfolk VA**

**INDUSTRY DAY
18 March 2025
1300-1430**

AGENDA

<u>Time</u>	<u>Action</u>	<u>Presenter</u>
1300	Opening Remarks/Introductions	NAVFAC Contracting
1305	Ground Rules and Goals	NAVFAC Contracting
1310	Project Presentation	NAVFAC Design Team
1400	Questions	NAVFAC Contracting
1430	Adjourn	

INTRODUCTIONS

- Philip Cole, Contracting Officer, NAVFAC Mid-Atlantic
- Kristy Gerrek, Contract Specialist, NAVFAC Mid-Atlantic
- Robert Brown, Project Manager, NAVFAC Mid-Atlantic
- Anthony Wilkins, Design Manager, NAVFAC Mid-Atlantic
- Christine Carlson, Associate VP, Principle; Project Manager, AECOM
- Kristi Guilfoyle, Project Manager, AECOM
- Bill Clendenin, Project Director, AECOM



GROUND RULES

- This meeting is informational and for planning purposes only.
- This is not a Request For Proposal (RFP). Discussions today will not be evaluated in response to any future requests for proposals.
- Do not provide the Government with proprietary information, trade secrets, or any other information deemed source selection sensitive, or information that you do not want disseminated to the public.
- Effort that any contractor/entity expends on this effort is at its own time, risk, and expense.
- Hold all questions until the end of the presentation.
- Everything you see today is a DRAFT and is subject to change.

INDUSTRY DAY GOALS

- Notify the Industry of the upcoming solicitation for the RM24-3467 Renovate SP17 for Fleet Legal Services, Naval Station Norfolk, Virginia.
- Inform Industry of the scope and possible construction challenges for the project.
- Solicit private sector input to help shape the project procurement.


PROJECT PRESENTATION

RM24-3467

NAVFAC / AECOM

RM24-3467

PROJECT LOCATION



Norfolk Naval
Station



SP-17 Building Site




NO. OF PERSONS	DESCRIPTION OF ACTIVITY
82 Personnel	Region Legal Service Office (RLSO)
5 Personnel	Navy-Marine Corps Trial Judiciary (NMCTJ)
43 Personnel	Defense Services Office (DSO)
28 Personnel	Tort Claims Unit (TCU)
24 Personnel	Claims (PCU)
17 Personnel	Claims (MCRU)
14 Personnel	Office of the Judge Advocate General of the Navy (OJAG)/ Naval Legal Service Command Headquarters Detachments (NLSC) HQ Dets Norfolk & Support
16 Personnel	Victim's Legal Counsel Program (VLCP)
29 Personnel	Office of the Special Trial Counsel (OSTC)
3 Personnel	Security Personnel
172 Visitors	RLSO, NMCTJ, DSO, VLCP, OSTC
MAXIMUM OCCUPANCY = 433 Total	261 Personnel / 172 Visitors




- **Total Area:**
 - Base Bid: 51,487 SF
 - Base Bid + Option 1: 65,525 SF
 - Base Bid + Option 1&2: 75,382 SF
 - Base Bid + Option 1, 2, 3: 109,348 SF
- **406 Parking Spaces + 20 Motorcycle Spaces outside the perimeter**
- **ICD/ICS 705, Marine Corps level II, and JPO security requirements**



BASE BID SITE PLAN

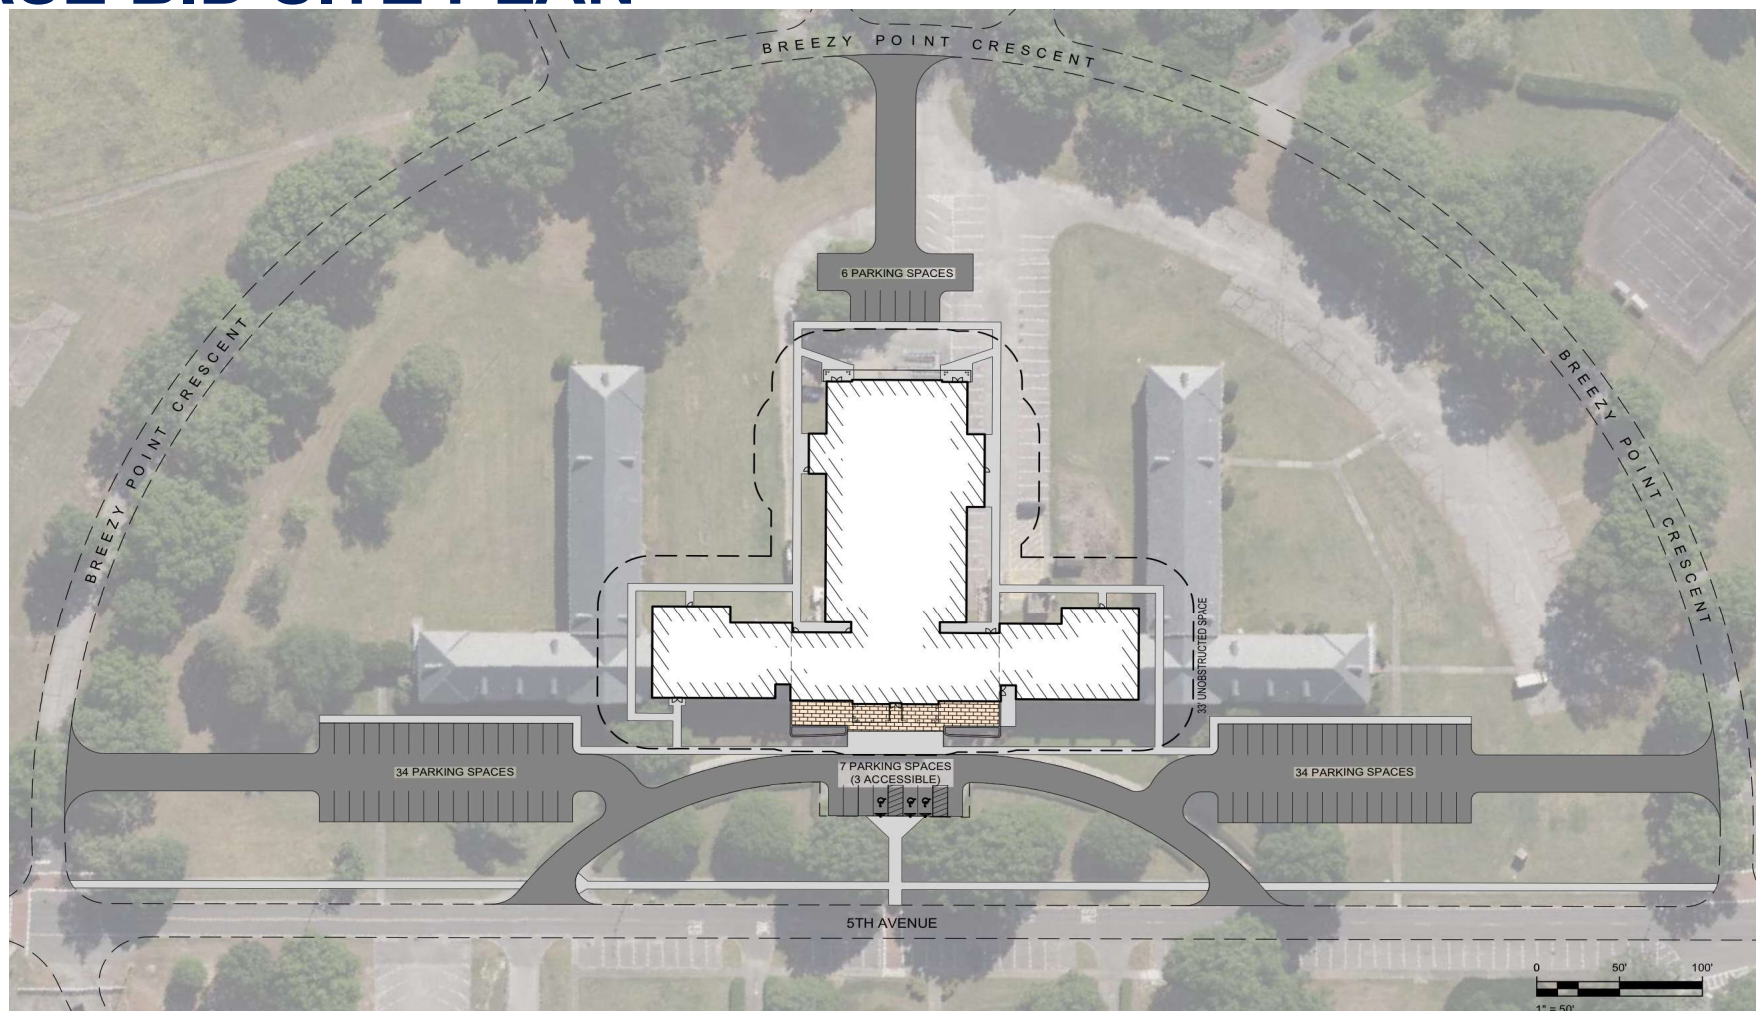


EXISTING FLOOR PLANS

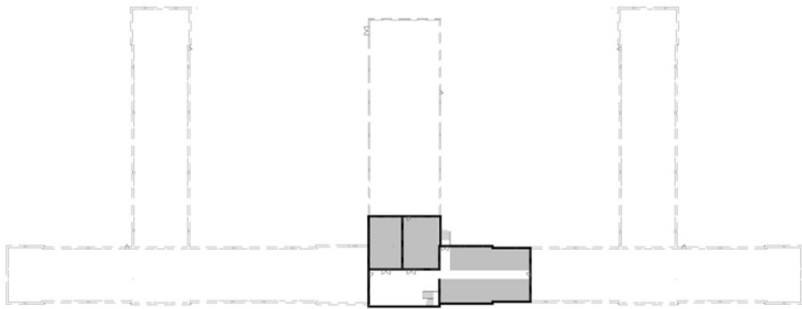


BASEMENT FLOOR PLAN

TOTAL FLOOR AREA (EXISTING): 6,378 GSF

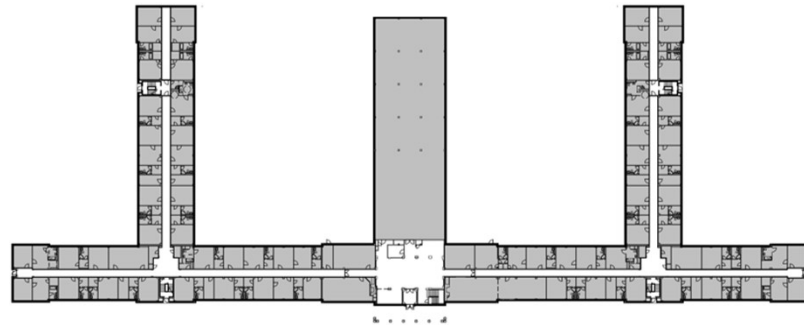


FIRST FLOOR PLAN

TOTAL FLOOR AREA (EXISTING): 47,488 GSF




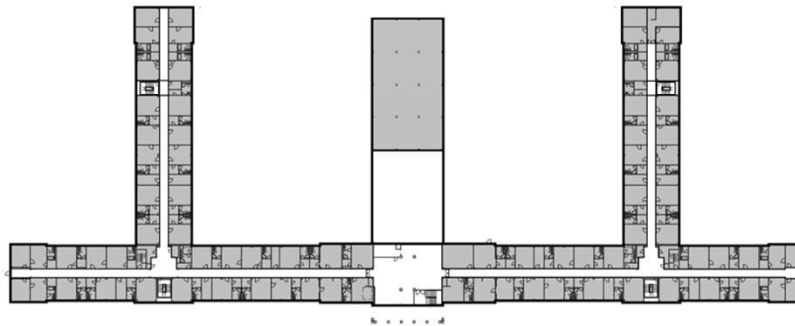


SECOND FLOOR PLAN

TOTAL FLOOR AREA (EXISTING): 44,089 GSF




SP-17 BASE BID + OPTIONS

	First Floor Plan	Second Floor Plan
Base Bid		
Option 1		
Option 2		
Option 3		


SPACE STACKING DIAGRAM

Integrating Remaining Element of SP-17 with New Construction (Base Bid + Options 1, 2 and 3)

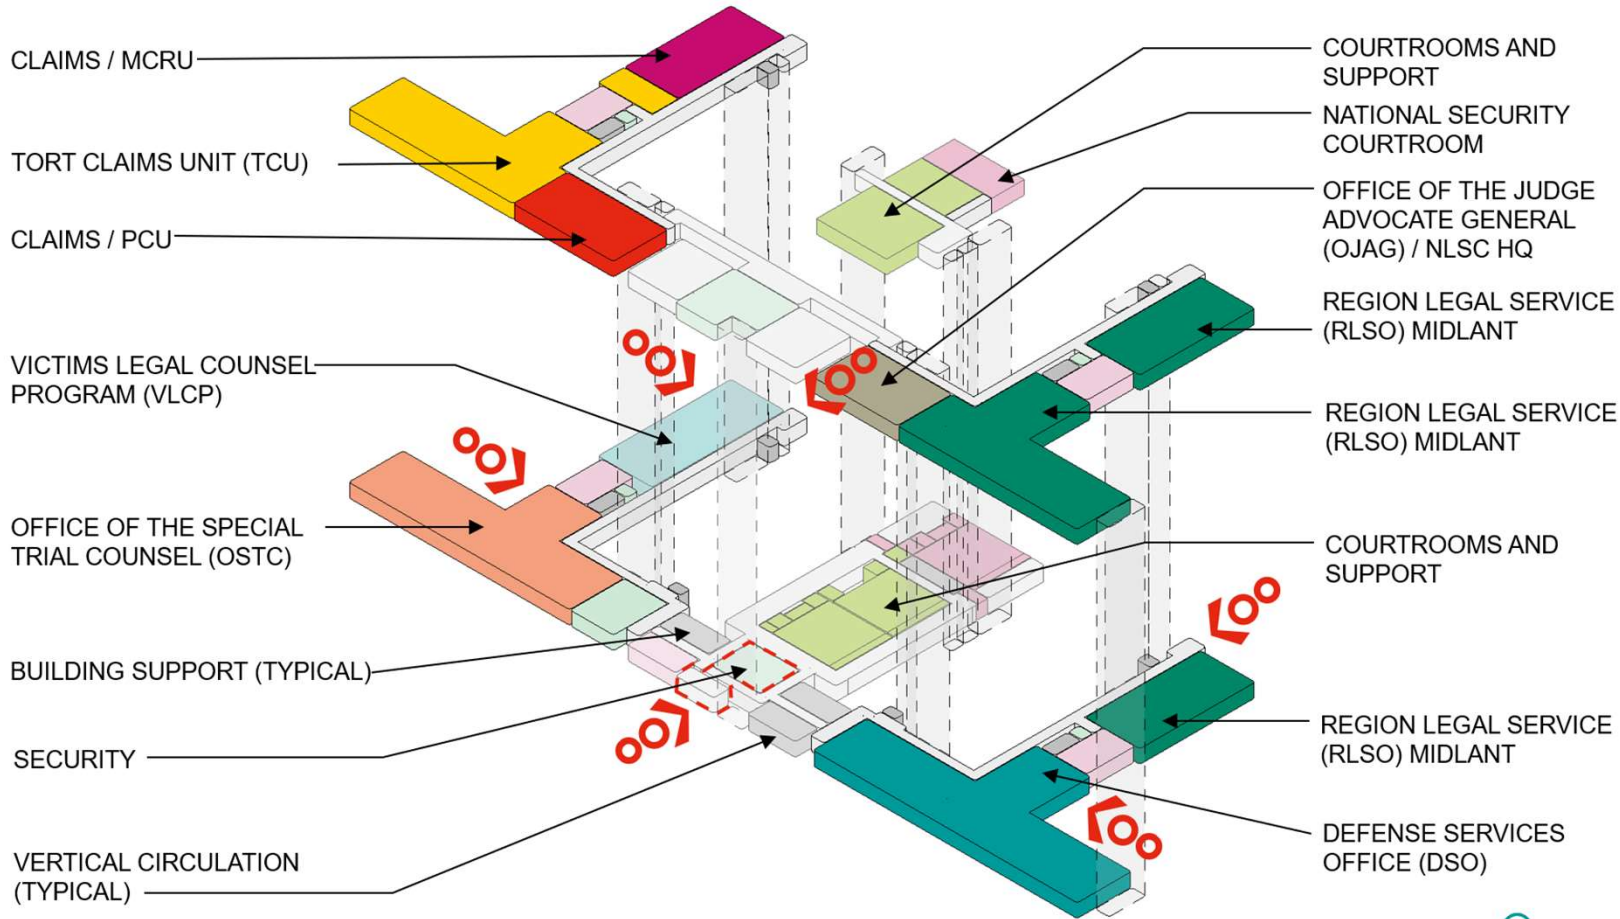


MASSING STUDY


Integrating Remaining Element of SP-17 with New Construction (Base Bid + Options 1, 2 and 3)

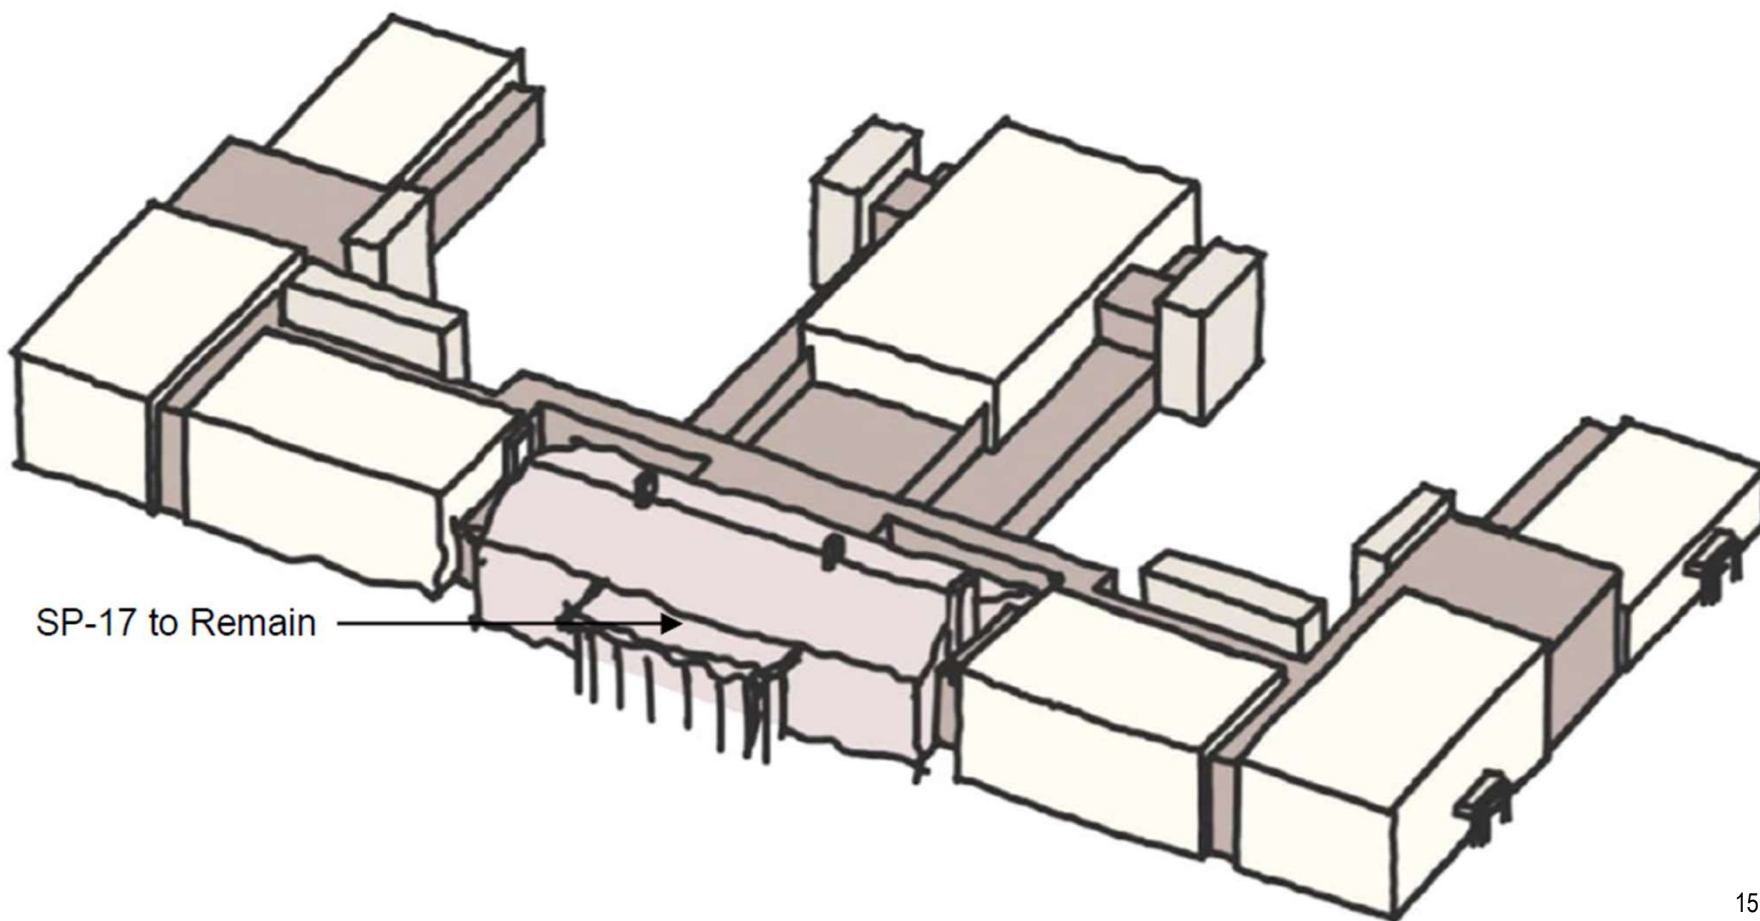


RENOVATION OF EXISTING TO REMAIN EXTERIOR

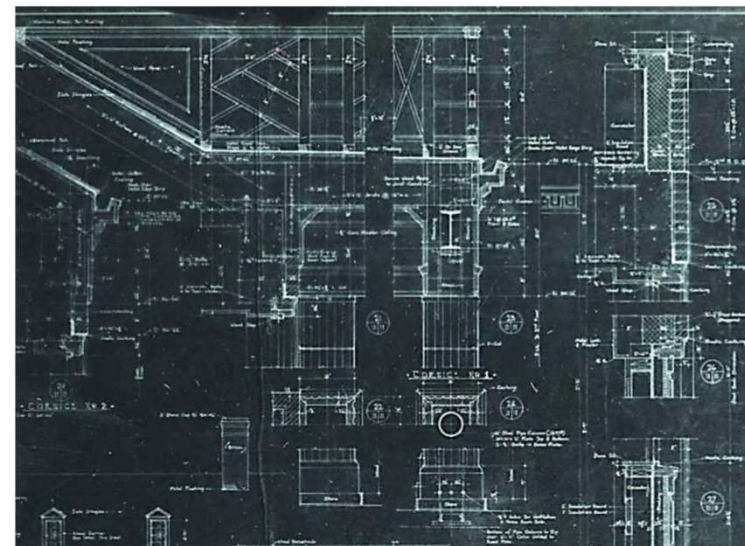

RESTORATION OF EXISTING TO REMAIN EXTERIOR

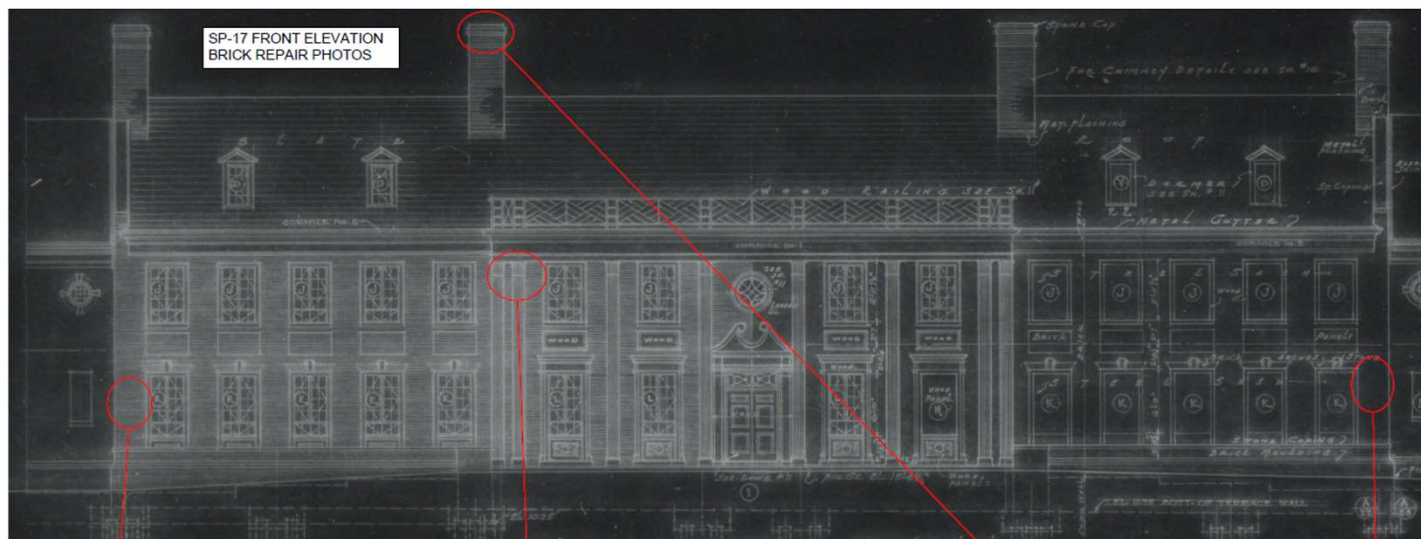


BUILDING FOOTPRINT CONSTRAINTS

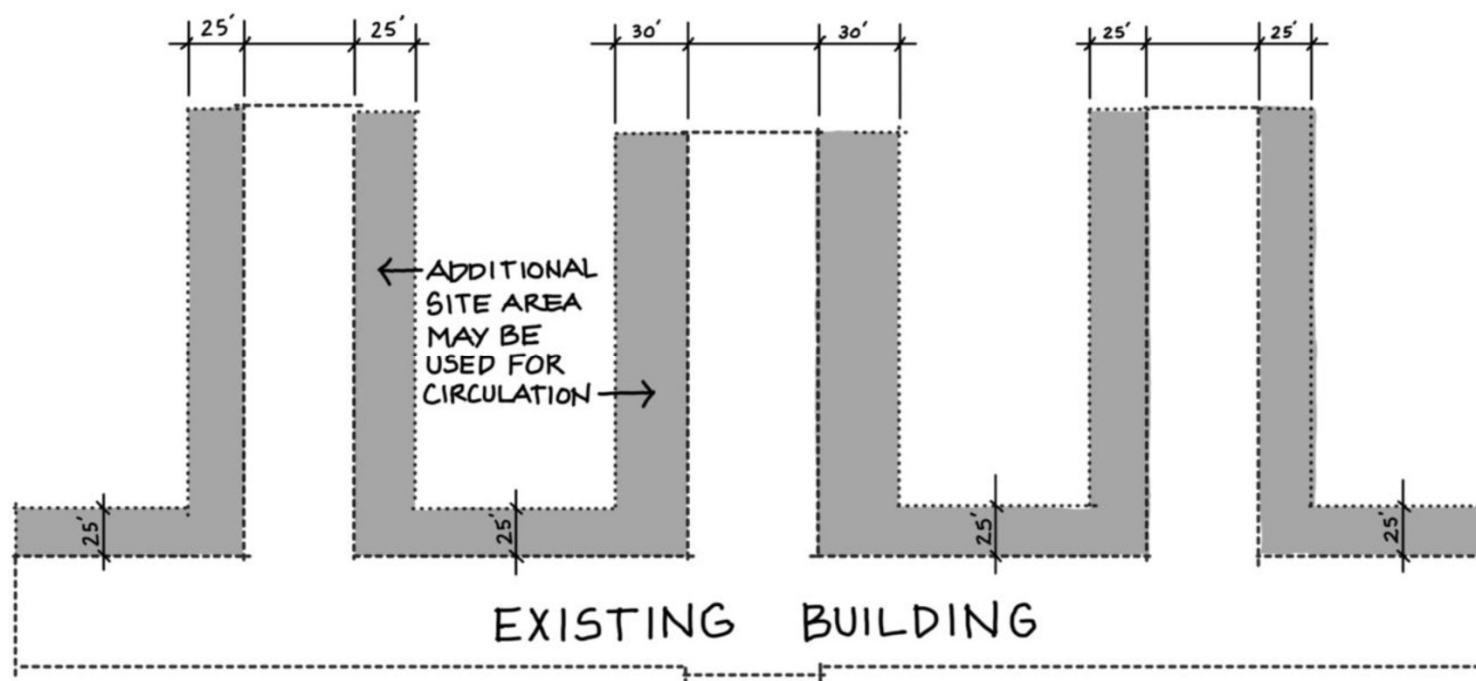

PROJECT CONSTRUCTION METHODOLOGY TYPES

Integrating Remaining Element of SP-17 with New Construction (Base Bid + Options 1, 2 and 3)

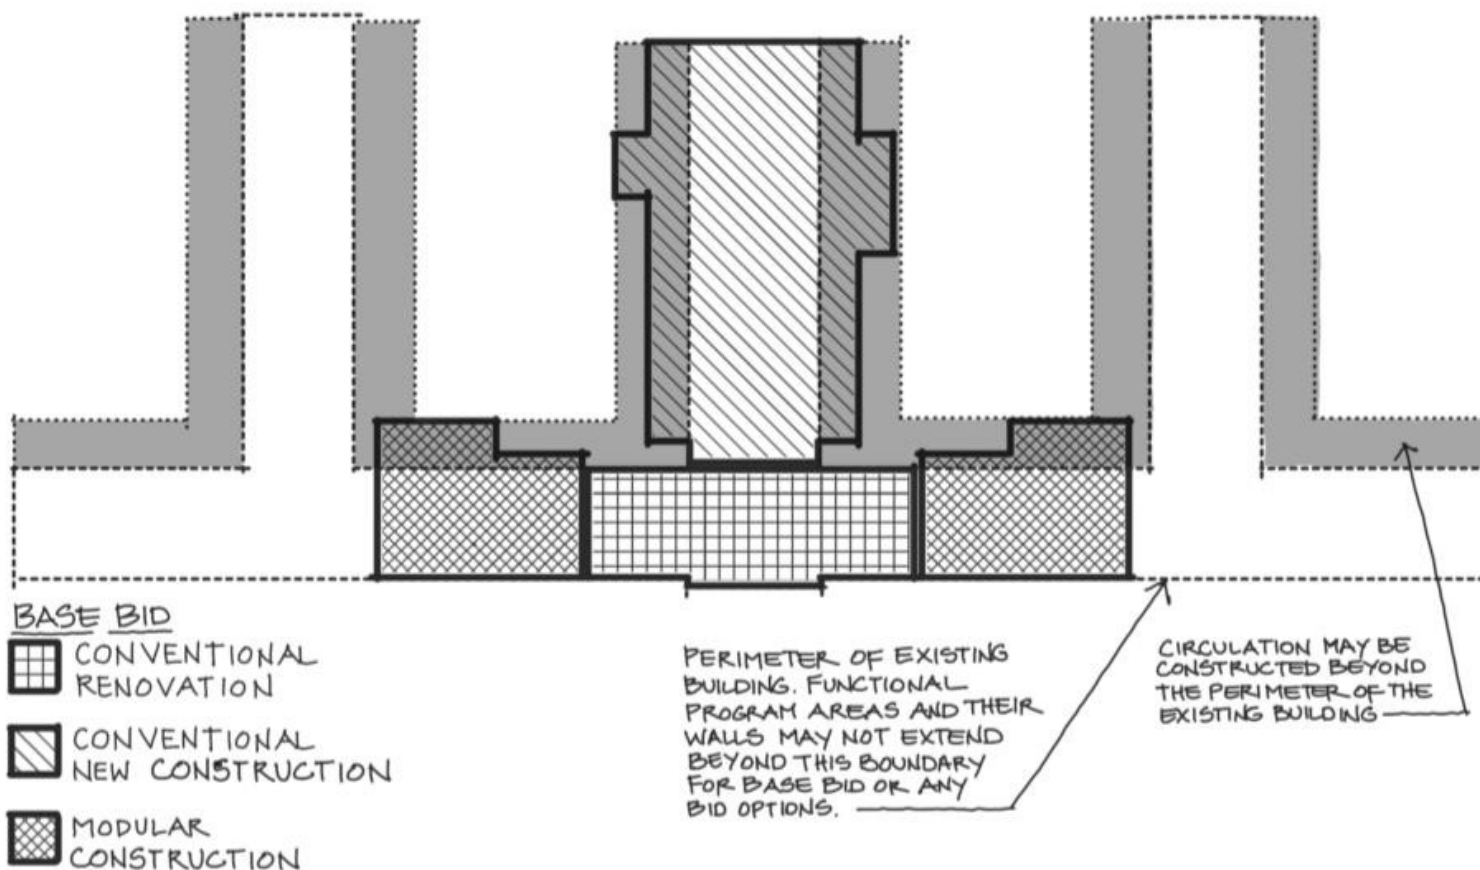

PROJECT CONSTRUCTION METHODOLOGY TYPES

Modular Construction

**Building elements constructed off-site,
in whole or in part, in a controlled environment and
assembled on-site.**

PROJECT CONSTRUCTION METHODOLOGY TYPES

Examples of permanent Modular construction

- Open “Shell” Modules
- Modular units partially finished in a factory
- Interior walls and finishes to be completed by general contractor on site




PROJECT CONSTRUCTION METHODOLOGY TYPES

Examples of permanent Modular construction


- Closed “Finished Box” Modules
- Interior of modular units are fully finished in a factory
- Exterior finish applied on site



Base bid: first floor plan

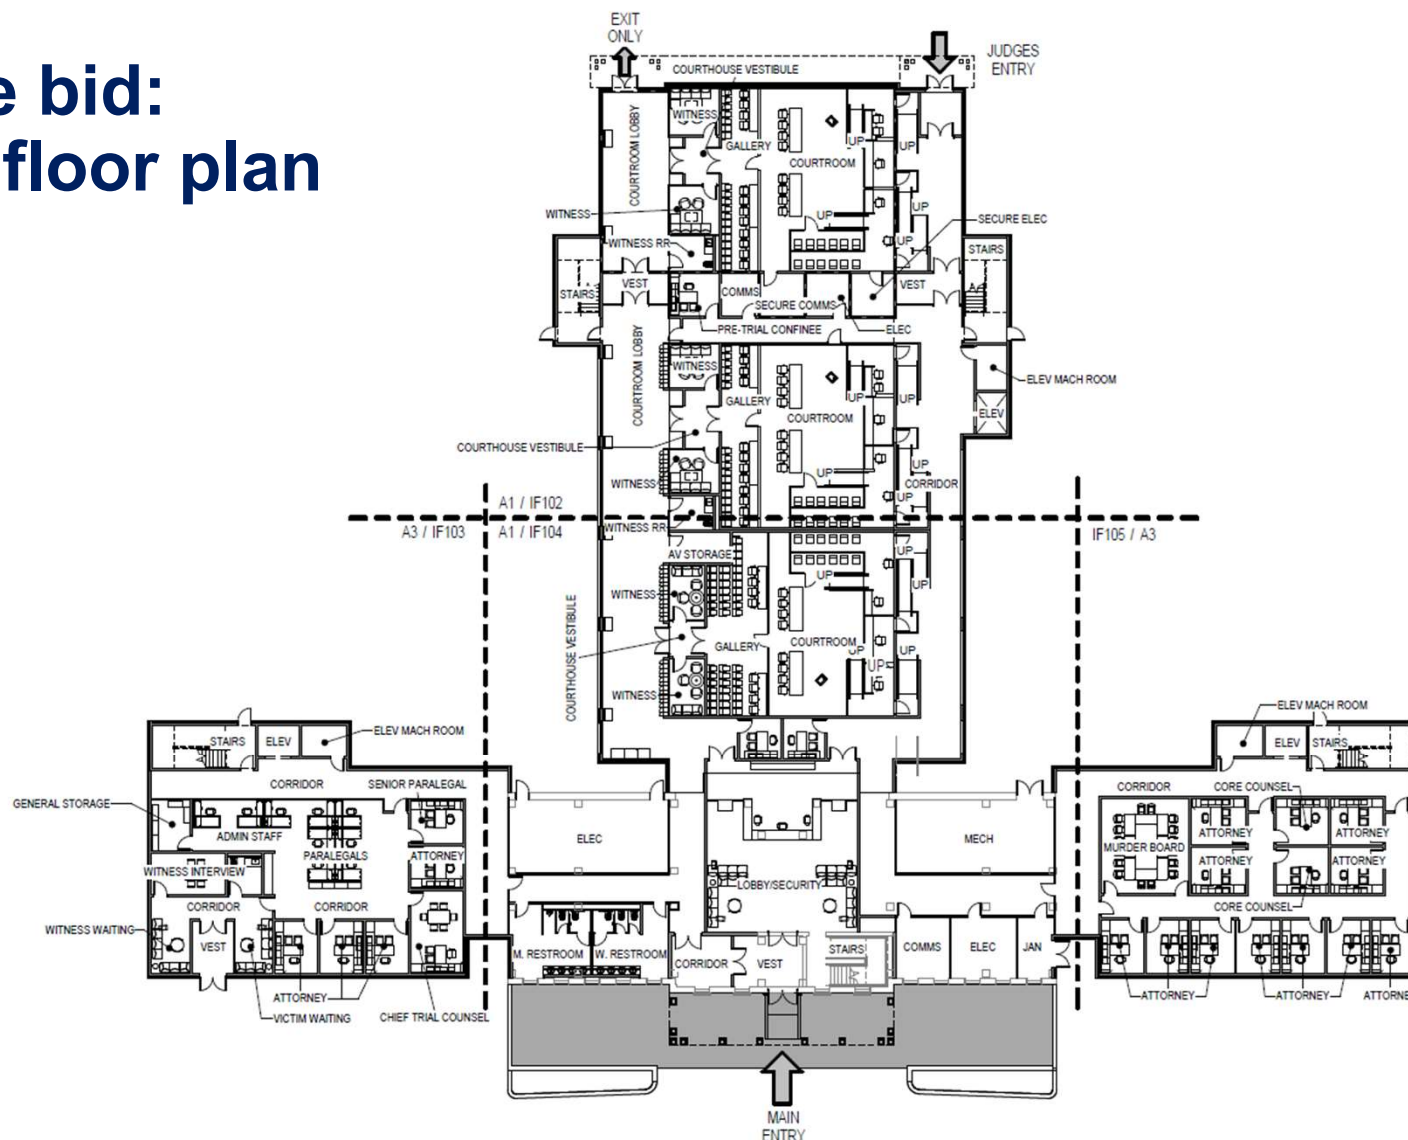

Base bid: second floor plan

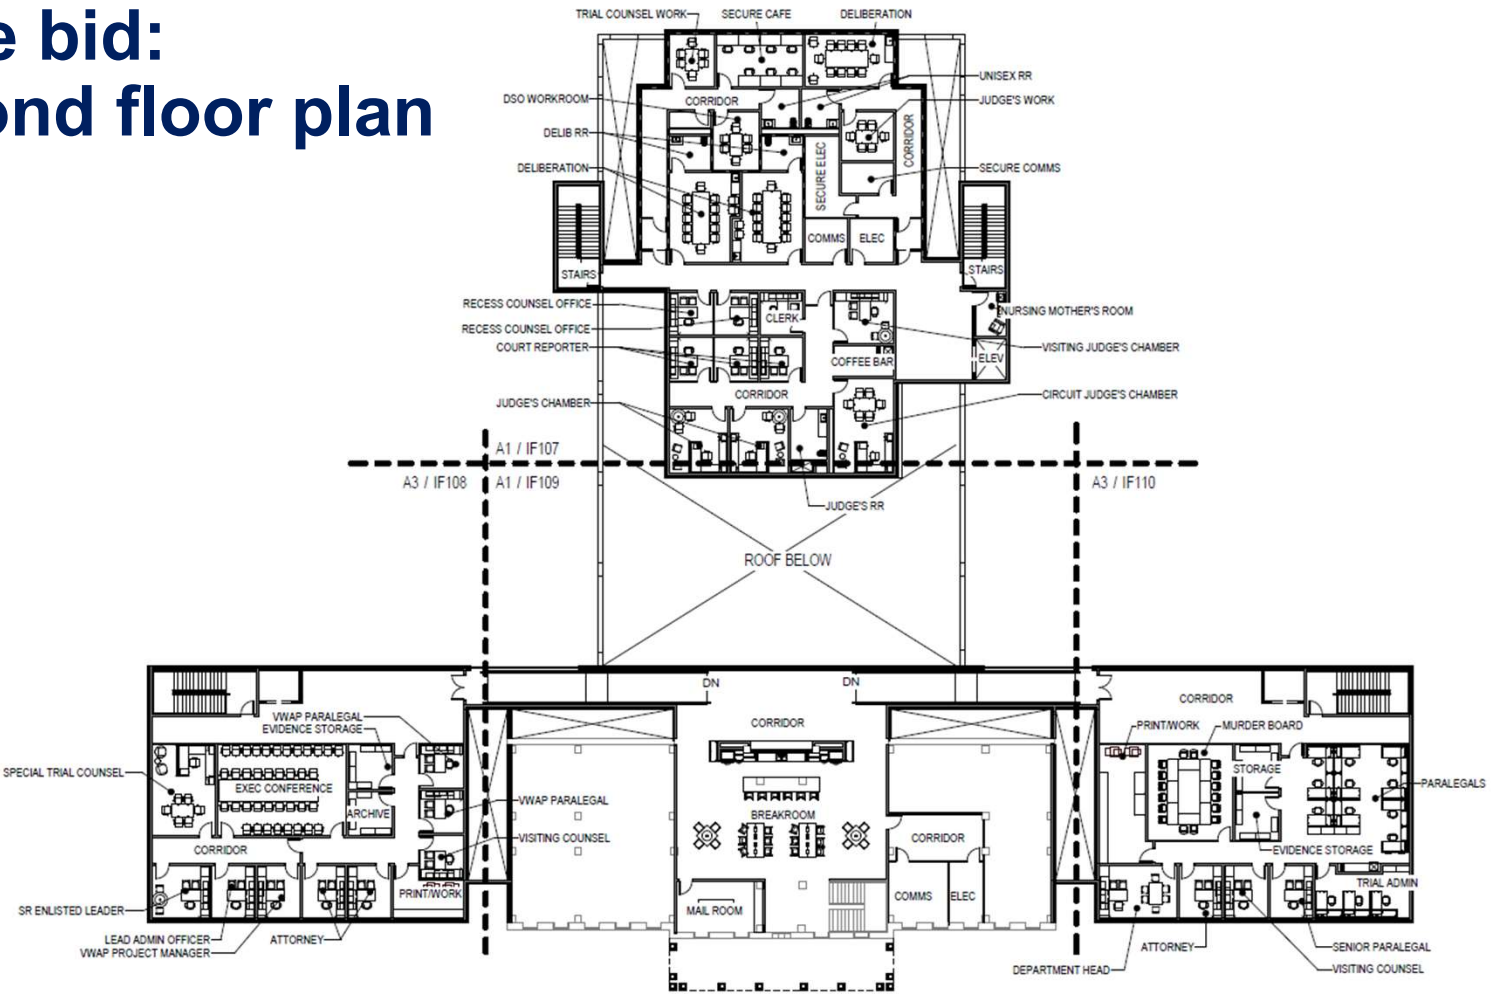

Base bid + option 1: First floor plan

THESE PROGRAM AREAS ARE NOT ACCOMMODATED	
RLSO HQ / COMMAND SERVICES / LEGAL ASSISTANCE	
VICTIMS LEGAL COUNSEL PROGRAM (VLCP)	
OJAG/ NLSC HQ	
CLAIMS (TCU, MCRU, AND PCU)	

First Floor:	35,764 SF
Second Floor:	29,561 SF
Total:	65,325 SF




Base bid + option 1: second floor plan

THESE PROGRAM AREAS ARE NOT ACCOMMODATED

RLSO HQ / COMMAND SERVICES / LEGAL ASSISTANCE
VICTIMS LEGAL COUNSEL PROGRAM (VLCP)
OJAG/ NLSC HQ
CLAIMS (TCU, MCRU, AND PCU)

First Floor:	35,764 SF
Second Floor:	29,561 SF
Total:	65,325 SF

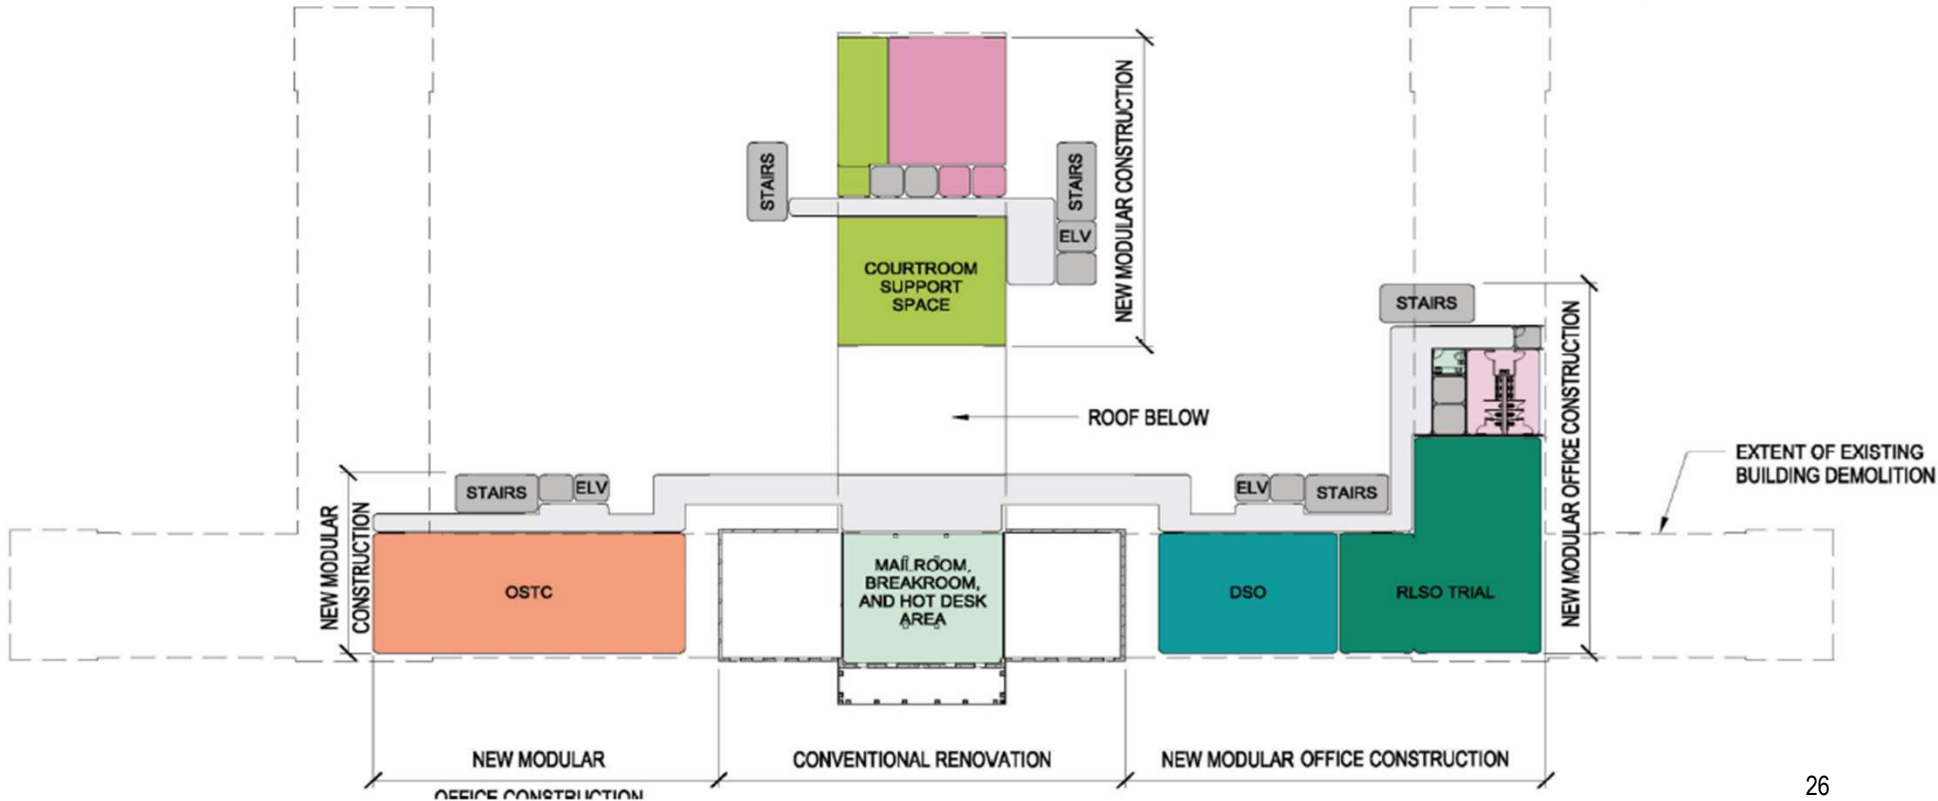

Base bid + option 1 & 2: First floor plan

THESE PROGRAM AREAS ARE NOT ACCOMMODATED	
RLSO HQ / COMMAND SERVICES / LEGAL ASSISTANCE	
OJAG/ NLSC HQ	
CLAIMS (TCU, MCRU, AND PCU)	


First Floor:	40,804 SF
Second Floor:	34,578 SF
Total:	75,382 SF



Base bid + option 1 & 2: second floor plan


THESE PROGRAM AREAS ARE NOT ACCOMMODATED	
RLSO HQ / COMMAND SERVICES / LEGAL ASSISTANCE	
OJAG/ NLSC HQ	
CLAIMS (TCU, MCRU, AND PCU)	

First Floor:	40,804 SF
Second Floor:	34,578 SF
Total:	75,382 SF

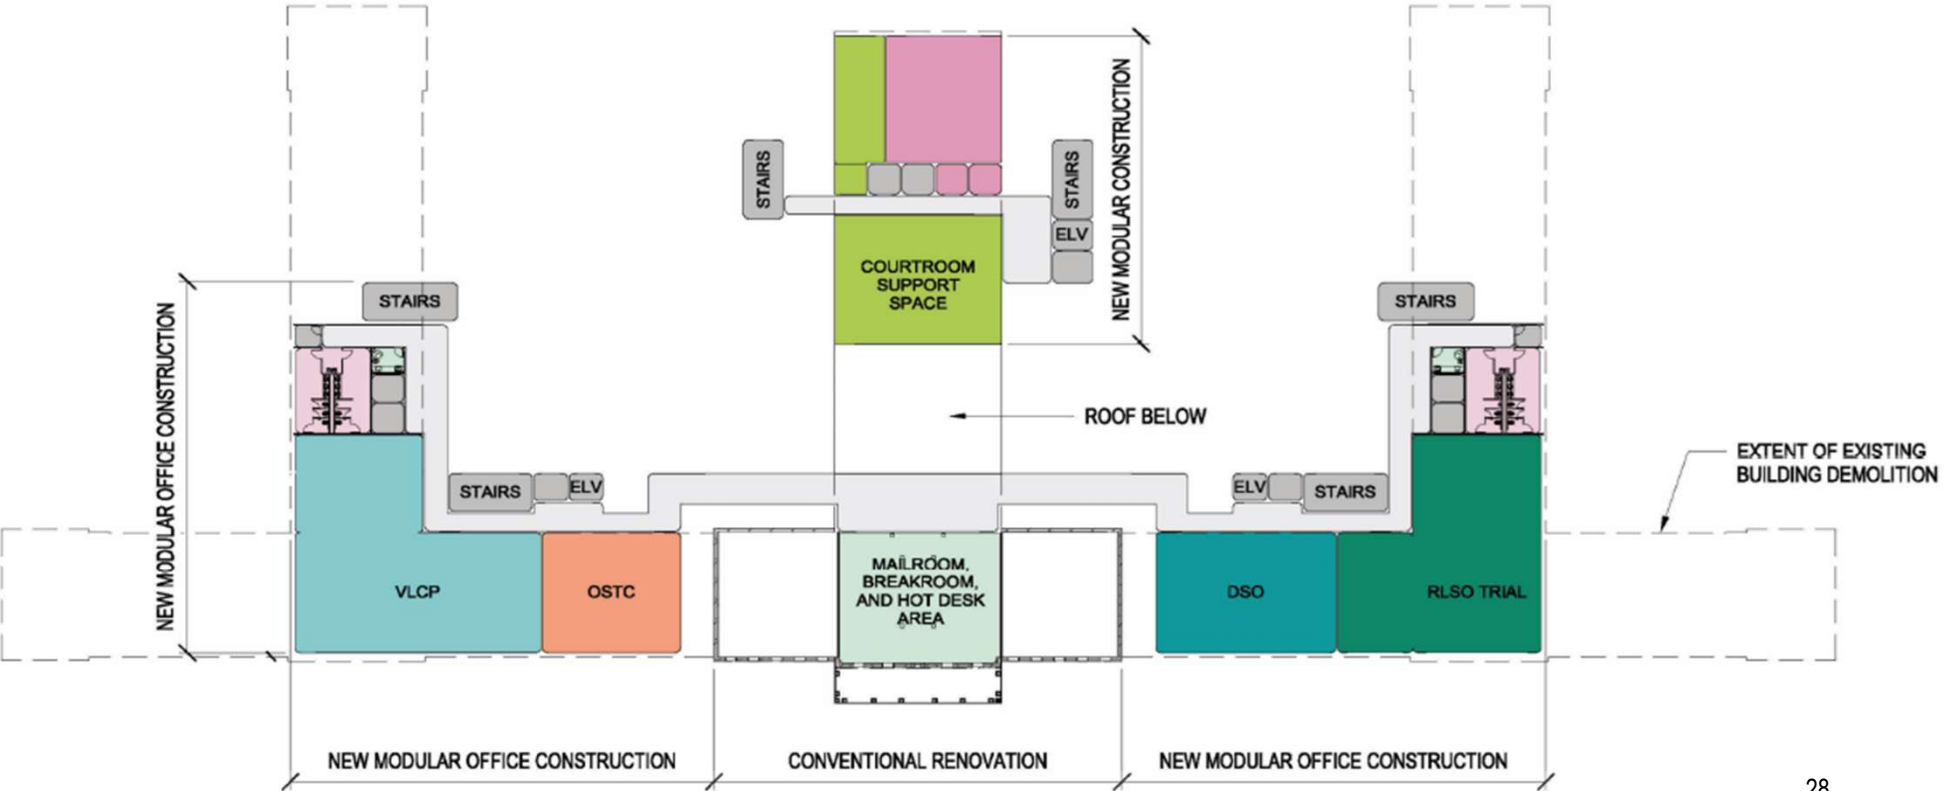


Base bid + option 1, 2 & 3: First floor plan

First Floor:	57,875 SF
Second Floor:	51,473 SF
Total:	109,348 SF

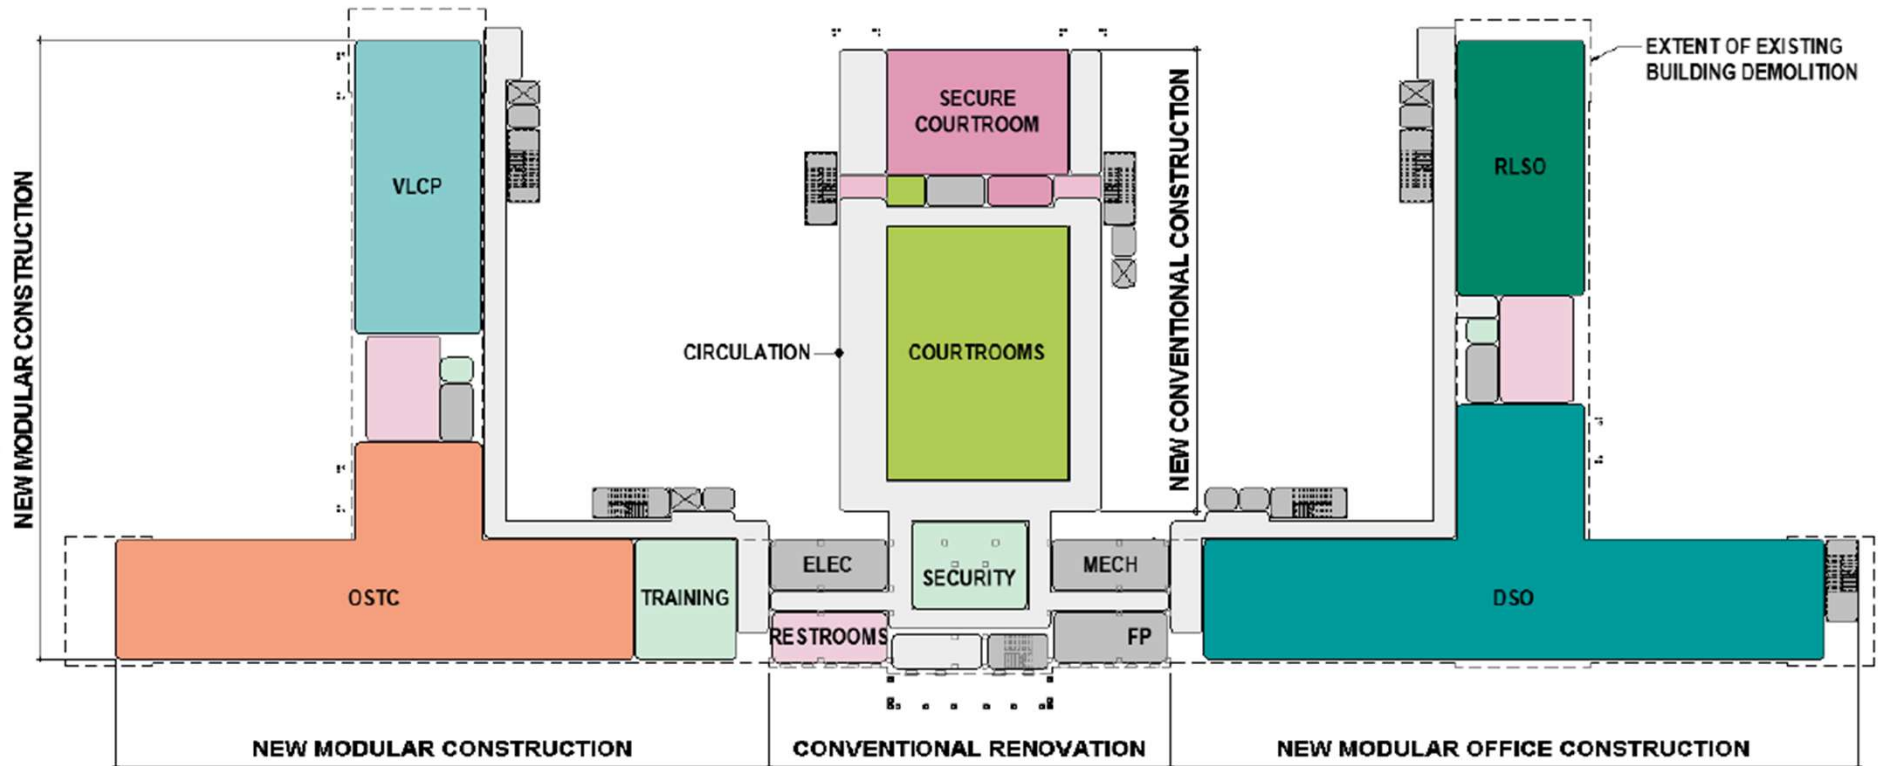

Base bid + option 1, 2 & 3: second floor plan

First Floor:	57,875 SF
Second Floor:	51,473 SF
Total:	109,348 SF

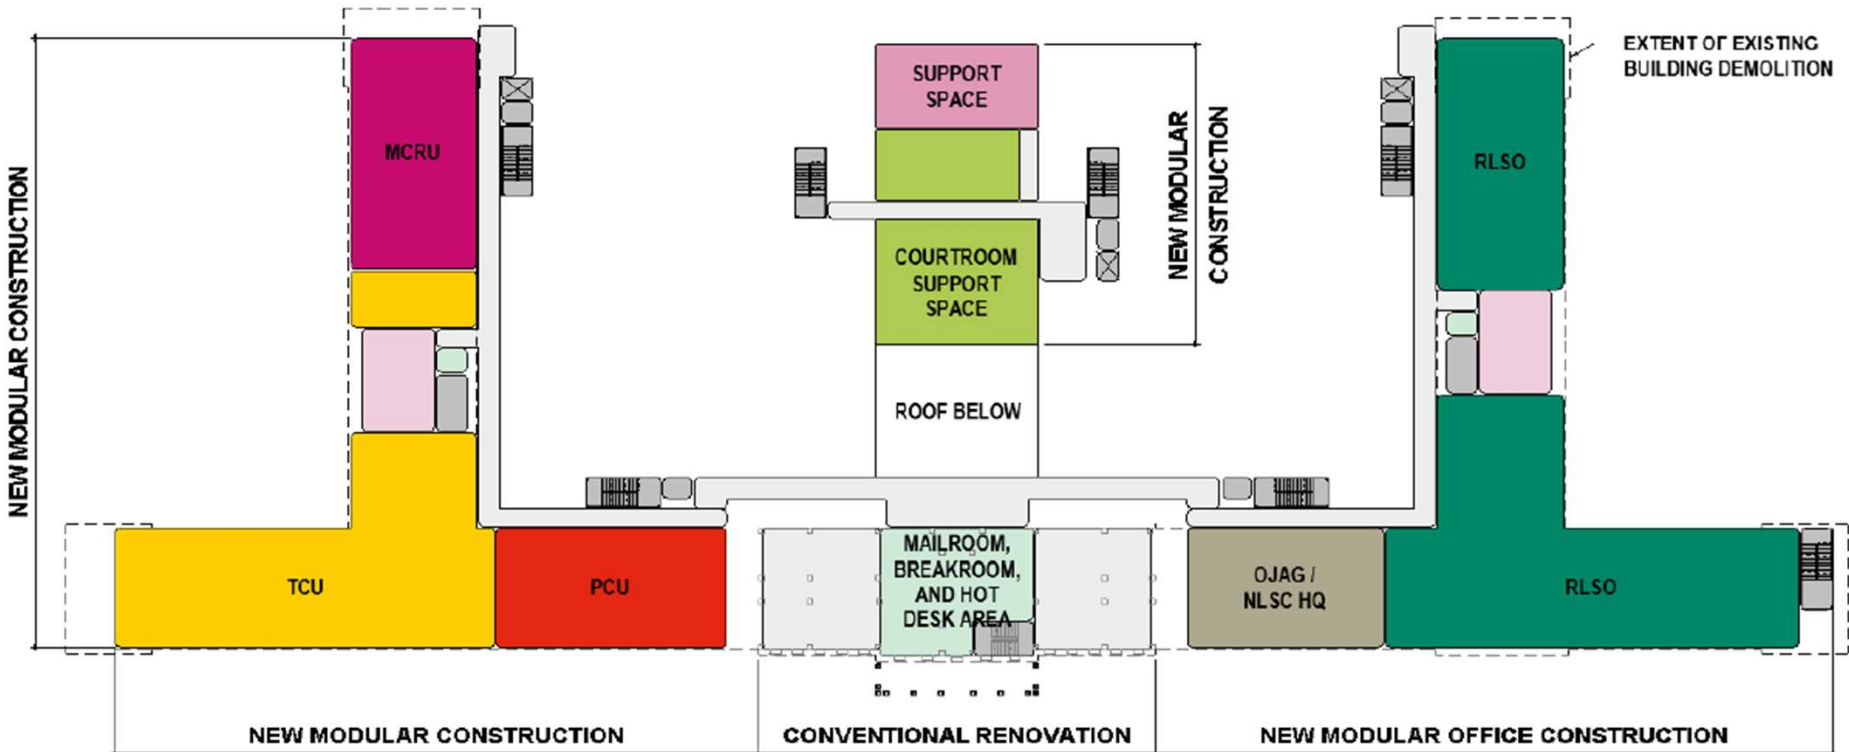

ANY QUESTIONS?

Any additional questions can be submitted in writing to:
Kristy.I.gerrek.civ@us.navy.mil

