



Navajo-Gallup Water Supply Project (NGWSP)

Remaining Projects

Industry Day
April 2, 2025


Bringing Water to People & Improving Lives



First water delivery planned by 2029

Agenda

- Overview Presentation (9:00 – 11:00 am)
 - Welcome
 - Navajo-Gallup Water Supply Project
 - ✓ Project Background
 - ✓ Project Status
 - ✓ Project Considerations
 - ✓ Remaining Projects
 - ✓ Project Overview
 - ✓ Acquisition Plan & Schedule
 - Questions
 - Tour Outline/JHA
- Lunch (11:00 am – 11:55 am)
- Meet back at San Juan College (12:00 pm)
- Site Tours (12:05 – 4:00 pm)

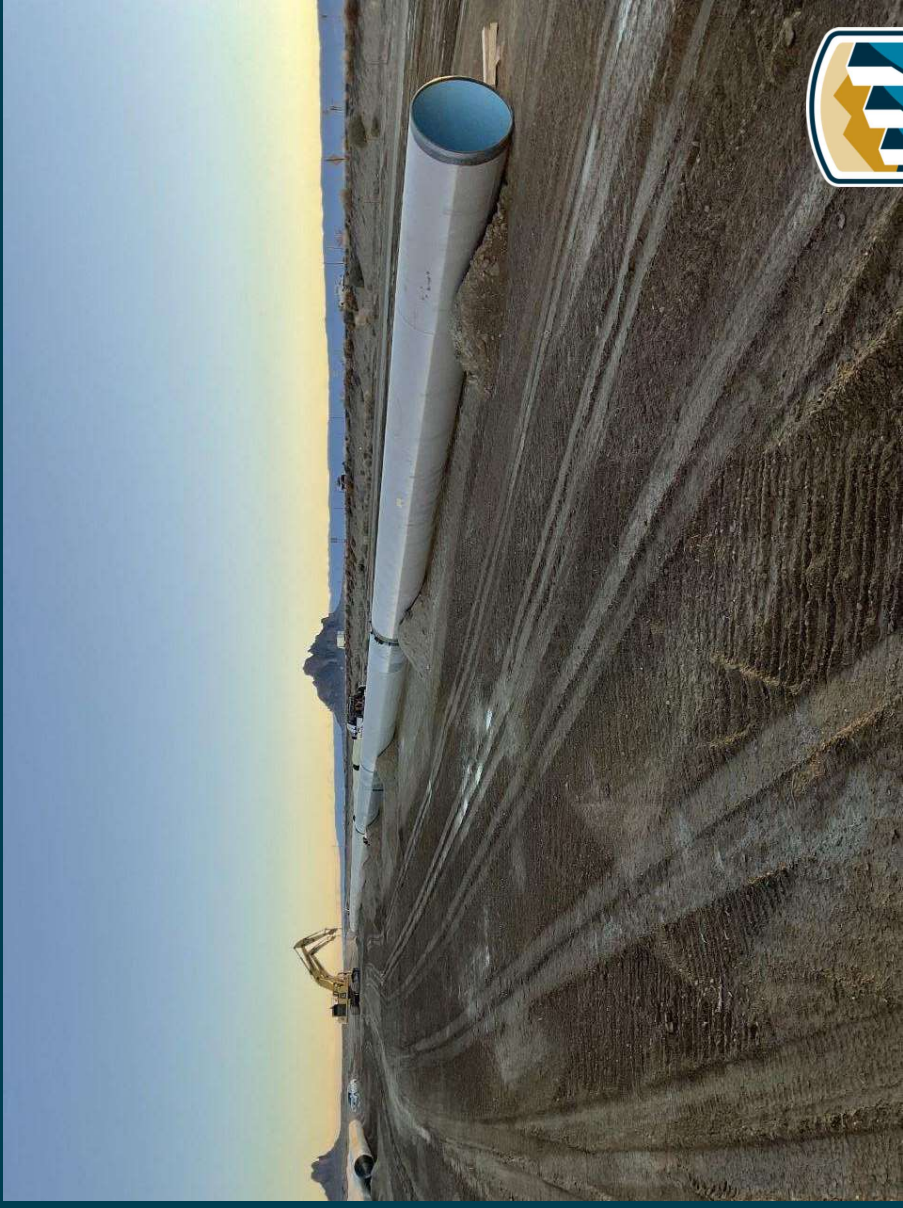

Goals for Industry Day

- Provide an overview of remaining NGWSP projects and contract requirements, highlighting the number of opportunities for contractors and suppliers
- Respond to potential offerors' inquiries

Disclaimer: Comments made during Industry Day - including this presentation - are not binding, refer to the RFQ/RFP documentation for final contract requirements.



USBR Team Introductions

Reclamation Technical Team Personnel

- Bart Deming (Four Corners Construction Office - Construction Engineer)
- Ryan Gladden (Four Corners Construction Office – Deputy Construction Engineer)
- Moncef Tihami (Four Corners Construction Office – Office Engineering Division Manager)
- Walt Shaw (Four Corners Construction Office – Contract Admin Chief)
- Emma Manzanares (Four Corners Construction Office – Field Engineering Division Manager) – Not in Attendance
- Hilda Castillo-Smith (Four Corners Construction Office – Resident Engineer)
- Malcolm Begay (Four Corners Construction Office - Civil Engineer)
- Gerald (Rod) Watkins (UCB Construction Safety Manager) – Not in Attendance



USBR Team Introductions

Reclamation Acquisitions Team Personnel

- Mike Verbitski (Chief, Interior Region 7 – UCB, Southern Group)
- Ashton Jones (Contracting Officer) - Not in Attendance (ajones@usbr.gov)
- Amy Loveless (Contracting Officer/Contract Specialist) (aloveless@usbr.gov)
- Philoma Singer (Contracting Officer/Contract Specialist)
- Melissa Trotter (Headquarters Small Business Specialist) - Not in Attendance
- Monica Burgio (Small Business Specialist, Interior Region 7 – UCB) - Not in Attendance



NGWSP Background/Need/Purpose

- Project has evolved over six decades
- Authorized for construction in March 2009 with passage of PL 111-11
- Cornerstone of the Navajo-San Juan Water Rights Settlement
- Largest project-based settlement (indexed ceiling) in U.S. history;
- Bureau of Reclamation charged with designing and constructing NGWSP
- Largest dollar project Reclamation has funded and built;

Public Law 111-11 111th Congress

An Act

To designate certain land as components of the National Wilderness Preservation System, to authorize certain programs and activities in the Department of the Interior and the Department of Agriculture, and for other purposes.

Mar. 30, 2009
[H.R. 146]

Be it enacted by the Senate and House of Representatives of the United States of America in Congress assembled,

Omnibus
Public Land
Management Act
of 2009.
16 USC 1 note.

SECTION 1. SHORT TITLE; TABLE OF CONTENTS.

(a) SHORT TITLE.—This Act may be cited as the “Omnibus Public Land Management Act of 2009”.

(b) TABLE OF CONTENTS.—The table of contents of this Act is as follows:

Sec. 1. Short title; table of contents.

PART III—NAVAJO-GALLUP WATER SUPPLY PROJECT

SEC. 10601. PURPOSES.

The purposes of this part are—

- (1) to authorize the Secretary to construct, operate, and maintain the Navajo-Gallup Water Supply Project;
- (2) to allocate the capacity of the Project among the Nation, the City, and the Jicarilla Apache Nation; and
- (3) to authorize the Secretary to enter into Project repayment contracts with the City and the Jicarilla Apache Nation.

SEC. 10602. AUTHORIZATION OF NAVAJO-GALLUP WATER SUPPLY PROJECT.


(a) IN GENERAL.—The Secretary, acting through the Commissioner of Reclamation, is authorized to design, construct, operate, and maintain the Project in substantial accordance with the preferred alternative in the Draft Impact Statement.

(b) PROJECT FACILITIES.—To provide for the delivery of San Juan River water to Project Participants, the Secretary may construct, operate, and maintain the Project facilities described in the preferred alternative in the Draft Impact Statement, including:




NGWSP Background/Need/Purpose


- Provide major infrastructure to secure and convey a long-term reliable drinking water supply for:
 - Eastern portion of the Navajo Reservation in New Mexico
 - Southwest portion of the Jicarilla Apache Reservation
 - City of Gallup
- Designed to meet current and future needs based on:
 - Population projections that assume increased growth rates as result of availability of water
 - Anticipated Housing and Business Growth




NGWSP Background/Need/Purpose

- Over 1/3rd of People Living on the Navajo Reservation haul drinking water to their homes
- Current drinking water is poor quality from groundwater
 - Some wells contaminated with arsenic and other hazardous elements
- Dwindling and unsustainable groundwater supplies

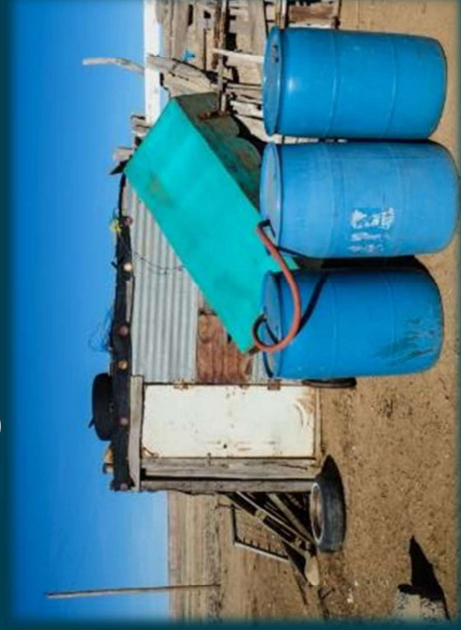

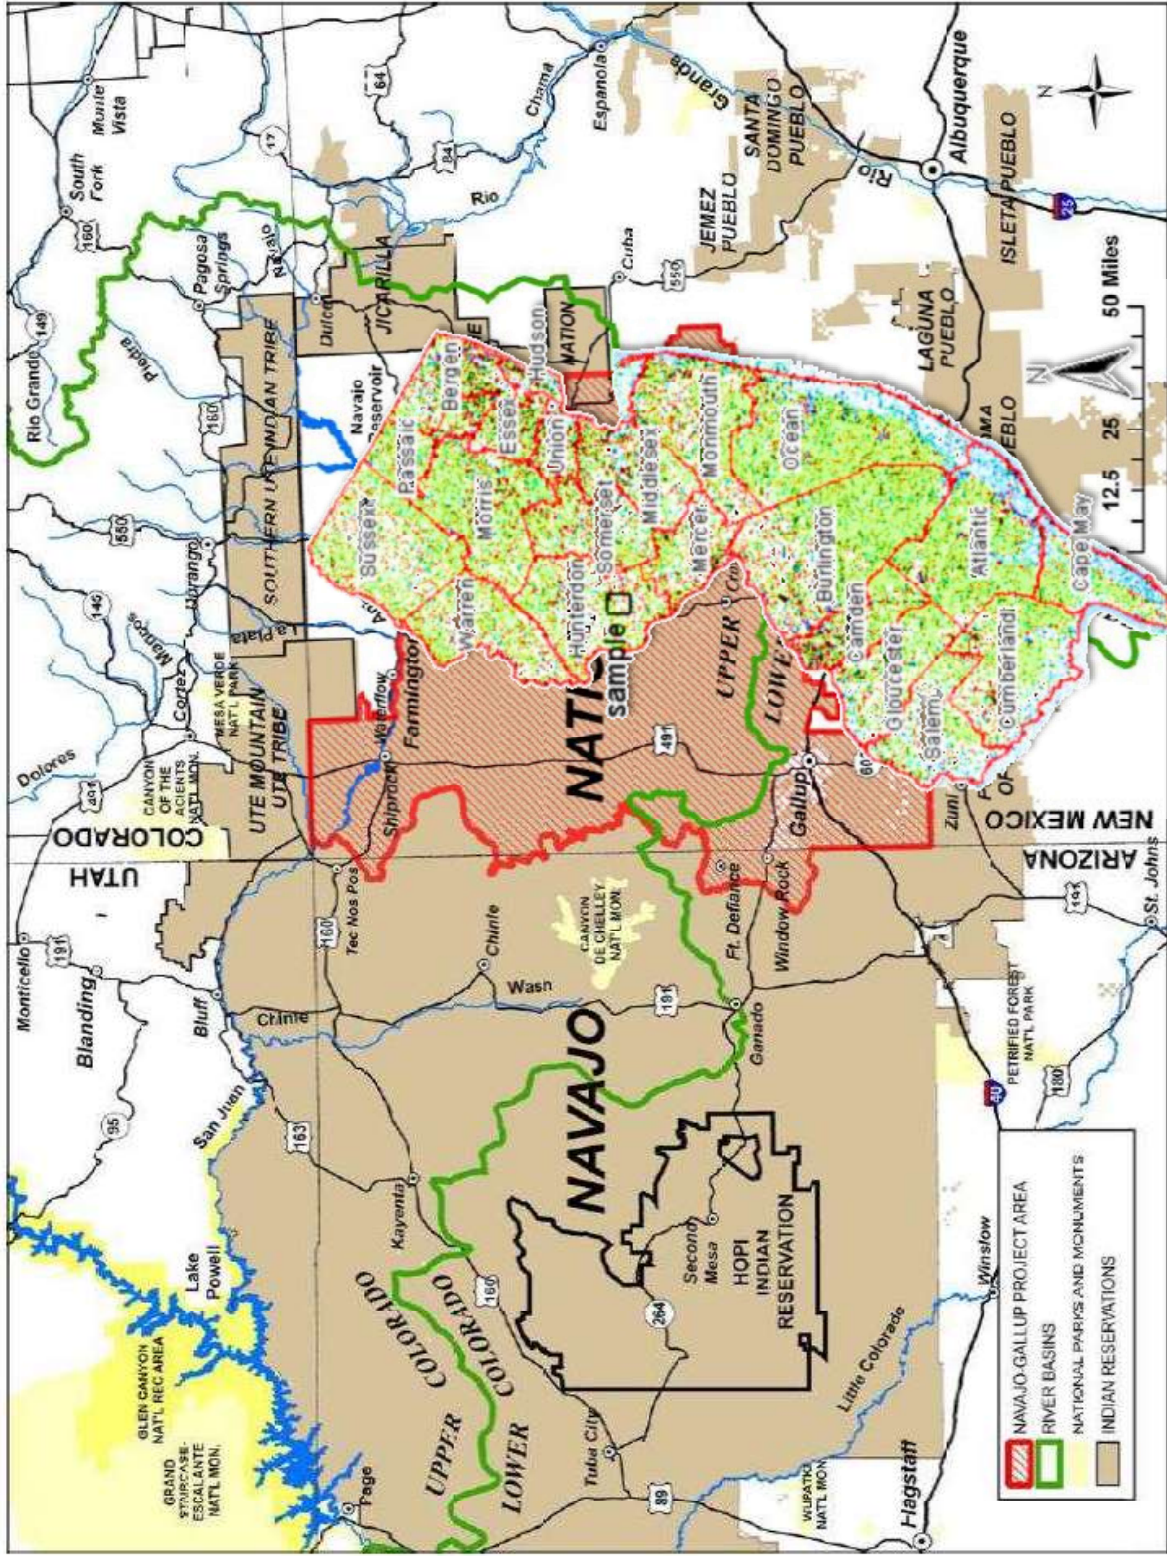

Project Details

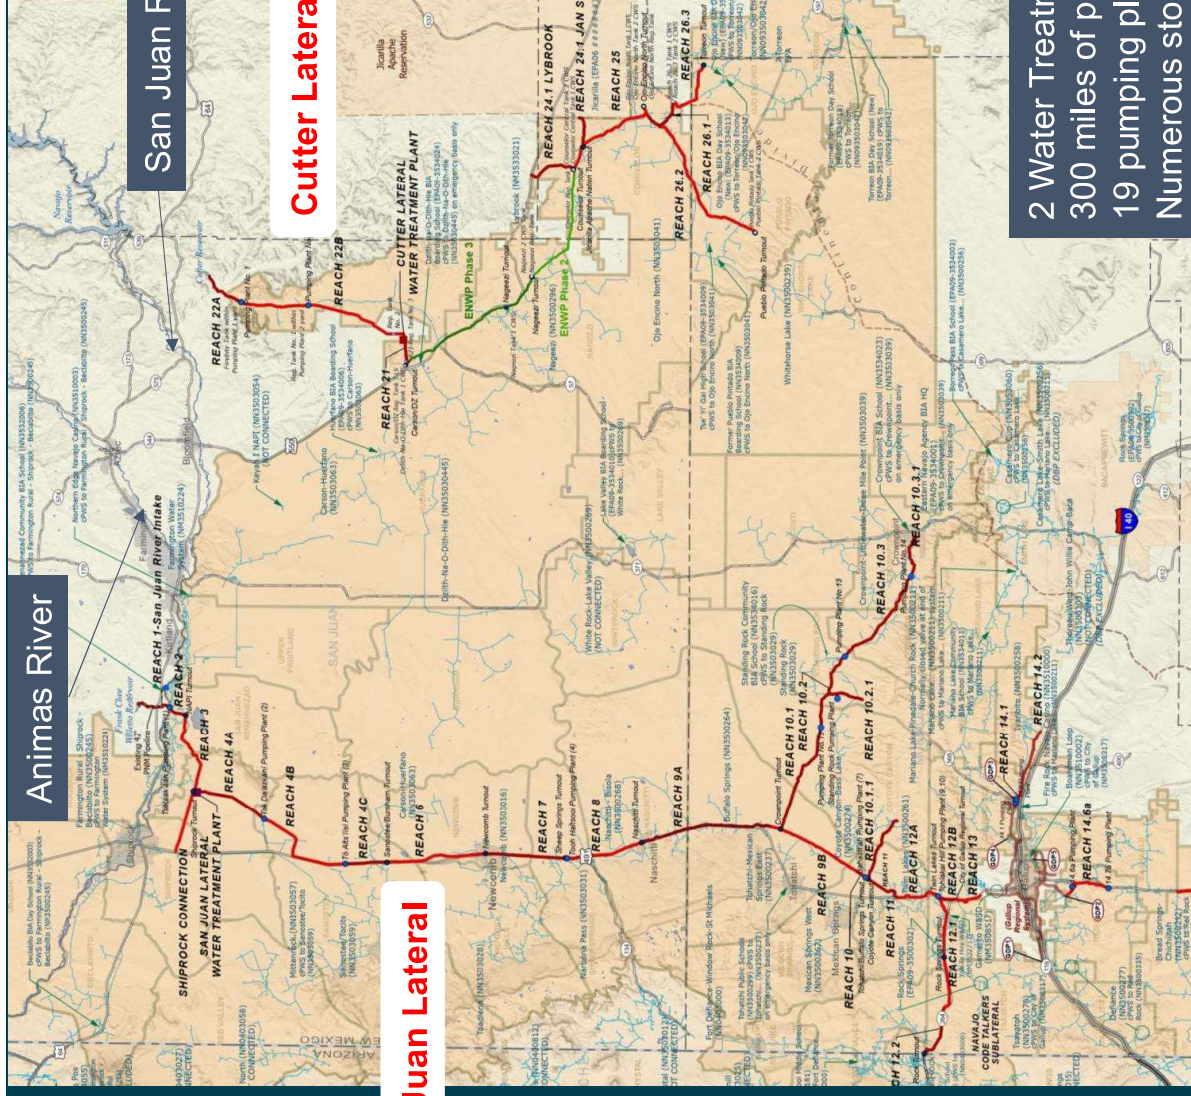

Animas River

San Juan River

Cutter Lateral


San Juan Lateral

2 Water Treatment Plants
300 miles of pipeline
19 pumping plants
Numerous storage tanks



Project Construction Details

- \$2.2 Billion – estimate (October 2023 price level)
- Being constructed by Reclamation, Navajo Nation, City of Gallup, and Indian Health Service w/Reclamation \$
- Facilities designed/constructed by others w/ non-Federal \$ using their own authorities:
 - Eastern Navajo Water Pipeline
 - Gallup Regional System

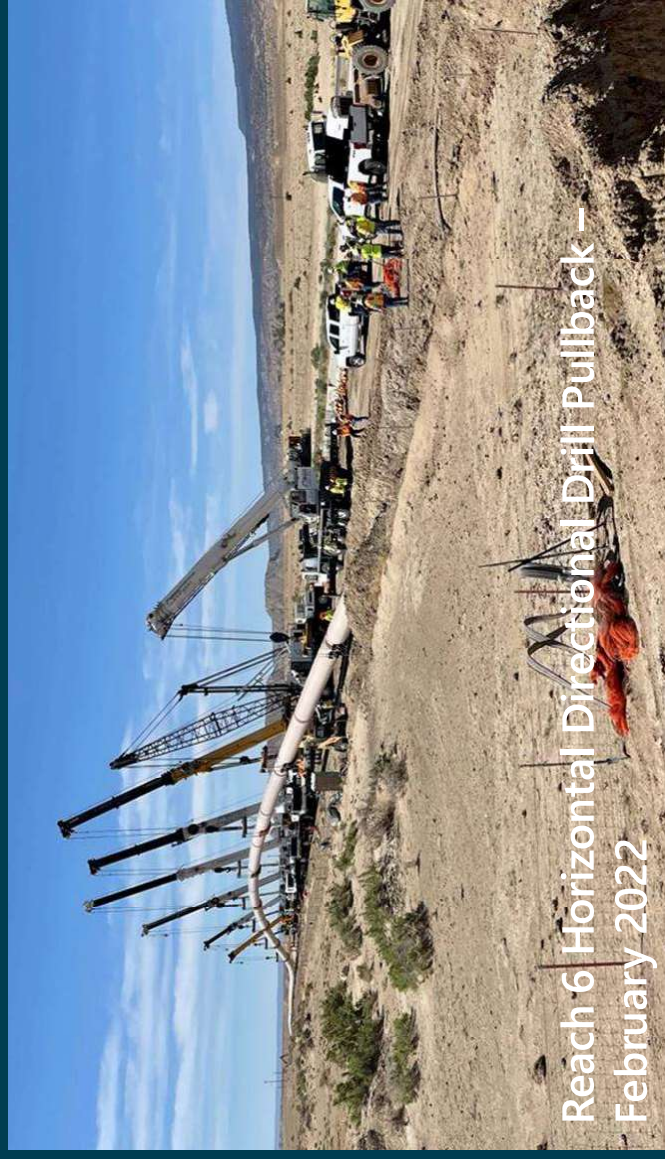

Reach 6 Horizontal Directional Drill Pullback –
February 2022



**Pumping Plants 4 & 7
Completion: April 2025**

Navajo Code Talkers

**Pumping Plants 2 & 3
Completion: Sept. 2025**


Cutter Lateral

San Juan Lateral

Operational
Completed
Under Construction
In Design
(As of March 2025)

Legend

 Navajo Nation Serviced Chapters
 Navajo Nation Non-Serviced Chapters
 Jicarilla Apache Reservation

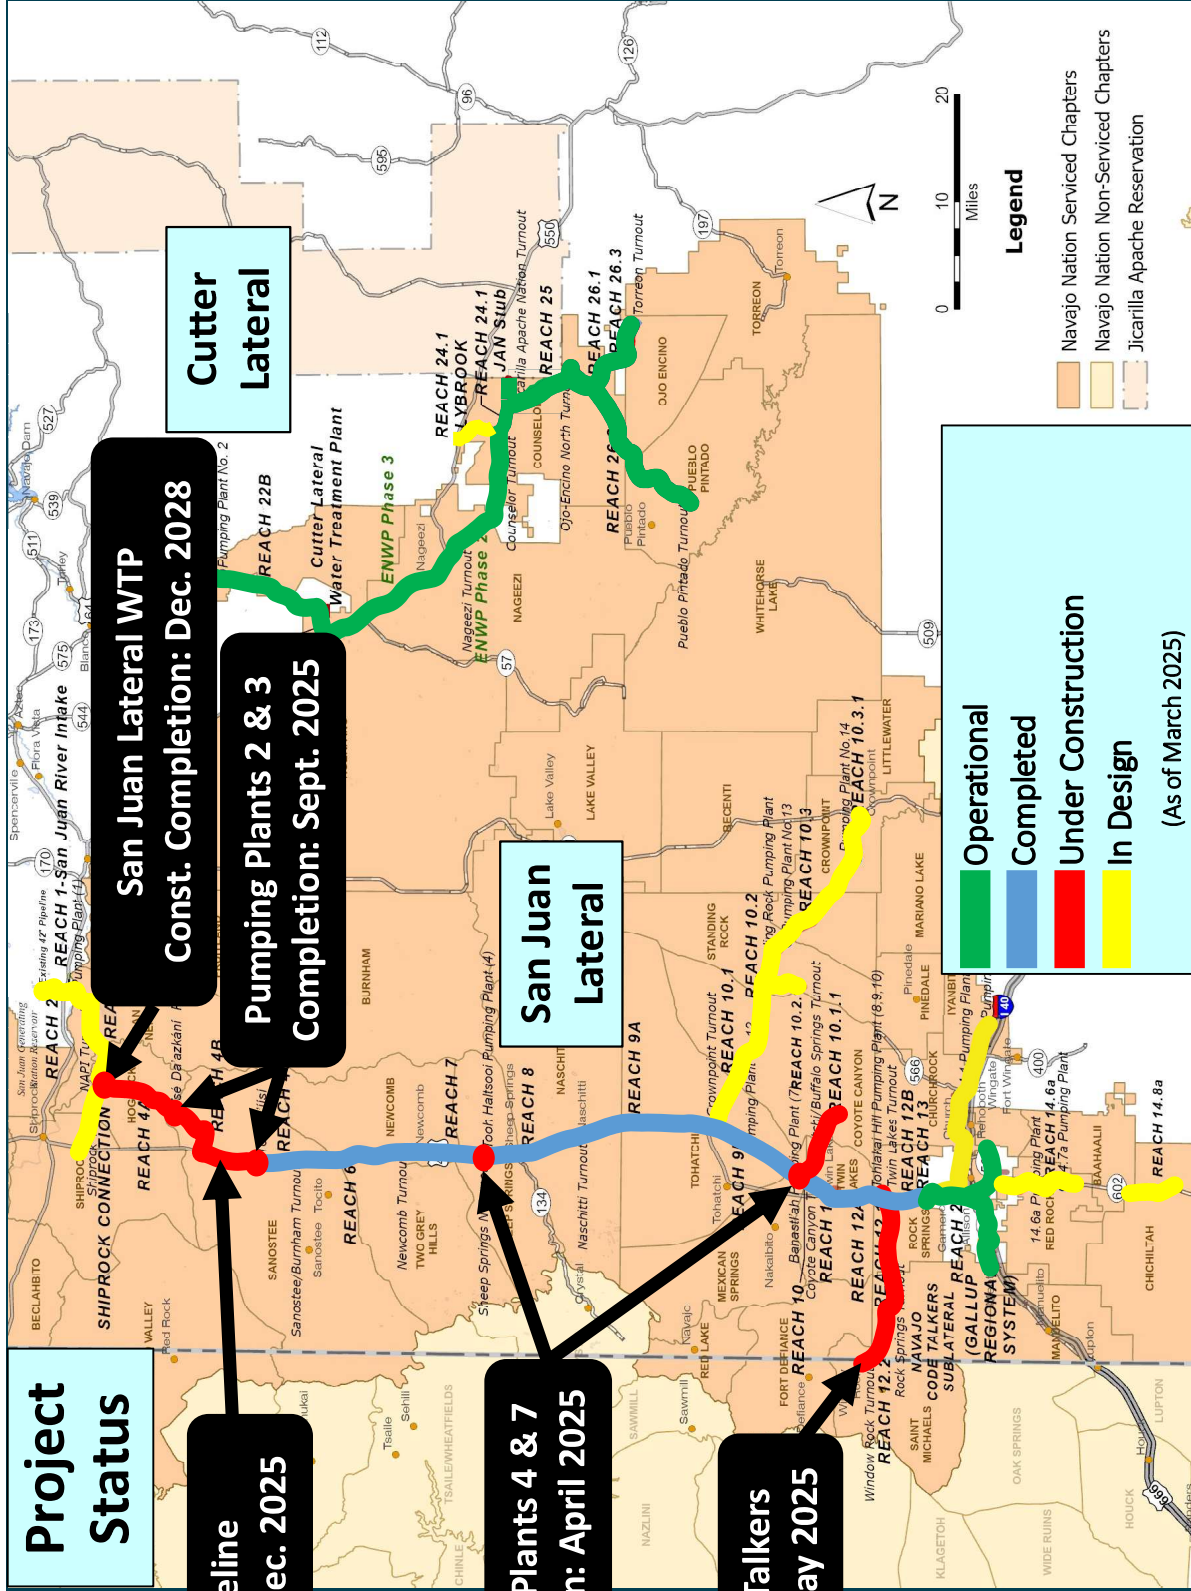

Status of Project Construction

Award Winning Cutter Lateral Water Treatment Plant:

- The CLWTP was recognized with 3 national awards in November 2021 by the Design-Build Institute of America (DBIA)
- The CLWTP was also recognized by Engineering News Record in April 2023 as the best water/environmental project in the nation.



Status of Project Construction

Award Winning 4C-8 Pipeline Project:

- ENR Southwest Regional Best Projects
 - Excellence in Safety Award and Award of Merit for Water/Environmental Project (NGWSP Block - 4c-8)



Project Considerations

- Quality Control (FAR Clause 52.246-12)
 - Contractor Responsibility – Managed by the Contractor
 - Quality Assurance provided by Reclamation (testing, surveys, inspection, etc.)
- Quantity Surveys (FAR Clause 52.236-16)
 - Quantity survey data, notes, computations – quantity for progress payment verified against actual survey data
 - Progress and final as-built drawings/markups
 - Note: Progress as-builts, quantity backup data, and construction schedule are required for progress payments



Project Considerations

- Environmental and Cultural Resource Compliance
 - Highly sensitive and closely monitored
 - Be familiar with specification requirements and potential impacts
- Stay within the ROW – ROW has been carefully planned to avoid cultural sites and impacts
 - ROW restrictions may exist – understand at time of bid
- Cultural Resource monitoring and discoveries – Monitoring may be required and discoveries may occur



Project Considerations

- Taxes (FAR 52.229-3)
 - The contract price includes all applicable Federal, State, and local taxes with the exception of New Mexico Gross Receipts Tax and Navajo Nation Tax.
 - The Contractor's responsibility to ensure full compliance with tax laws
 - The tax filing documents/receipts must be submitted with the invoice to be reimbursed the taxes paid



Remaining NGWSP Construction Projects

REMAINING NGWSP PROJECTS					
Item #	Project	Solicitation	Award	Start of Construction	End of Construction
1	SJL Intake & River Pumping Plant	September 25, 2025	March 20, 2026	June 5, 2026	October 6, 2028
2	Reach 1 Bypass Tank	May 7, 2026	September 10, 2026	November 1, 2026	September 1, 2027
3	FCW Reservoir & Dam	May 10, 2027	September 13, 2027	November 1, 2027	May 1, 2028
4	Block 2-3 Pipeline	April 10, 2026	September 16, 2026	November 4, 2026	August 11, 2028
5	Block 2-3 HDD	October 29, 2025	April 22, 2026	June 10, 2026	August 24, 2027
6	Pumping Plant 1	June 24, 2025	November 11, 2025	January 27, 2026	May 30, 2028
7	Shiprock Connection	October 14, 2027	March 2, 2028	April 20, 2028	March 1, 2029
8	Turnout Buildings	June 5, 2027	October 23, 2027	December 11, 2027	August 25, 2028
9	Reach 14.6a, 14.7a, 14.8a Pipeline	February 11, 2028	June 30, 2028	August 18, 2028	June 29, 2029
10	DZ Booster / Tank	December 1, 2025	April 6, 2026	May 25, 2026	April 8, 2027

10 Remaining Construction Projects




Project Overview Map


- SJL Intake & River PP
- Reach 1 Bypass Tank
- FCW Reservoir & Dam
- Pumping Plant 1
- Block 2-3 Pipeline
- Block 2-3 HDD
- Shiprock Connection
- Turnout Buildings
- Reach 14.6a, 14.7a, 14.8a
- DZ Booster / Tank

FCWR

WTP

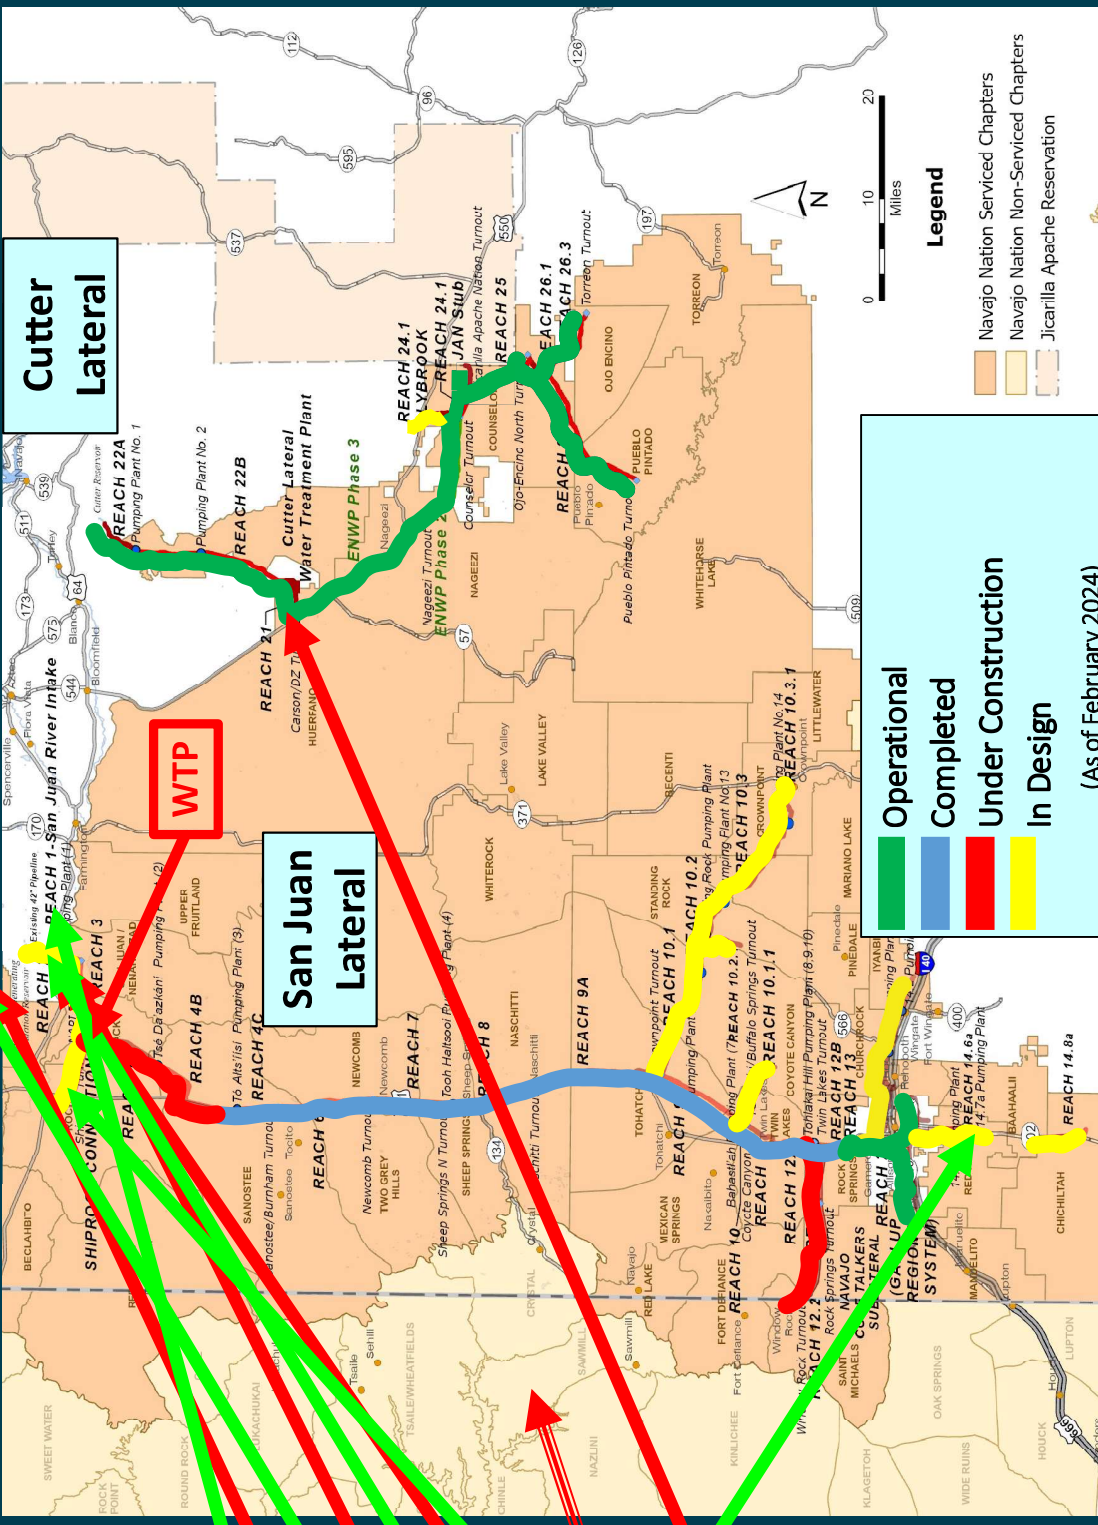

Project Overview Map - Raw Water System

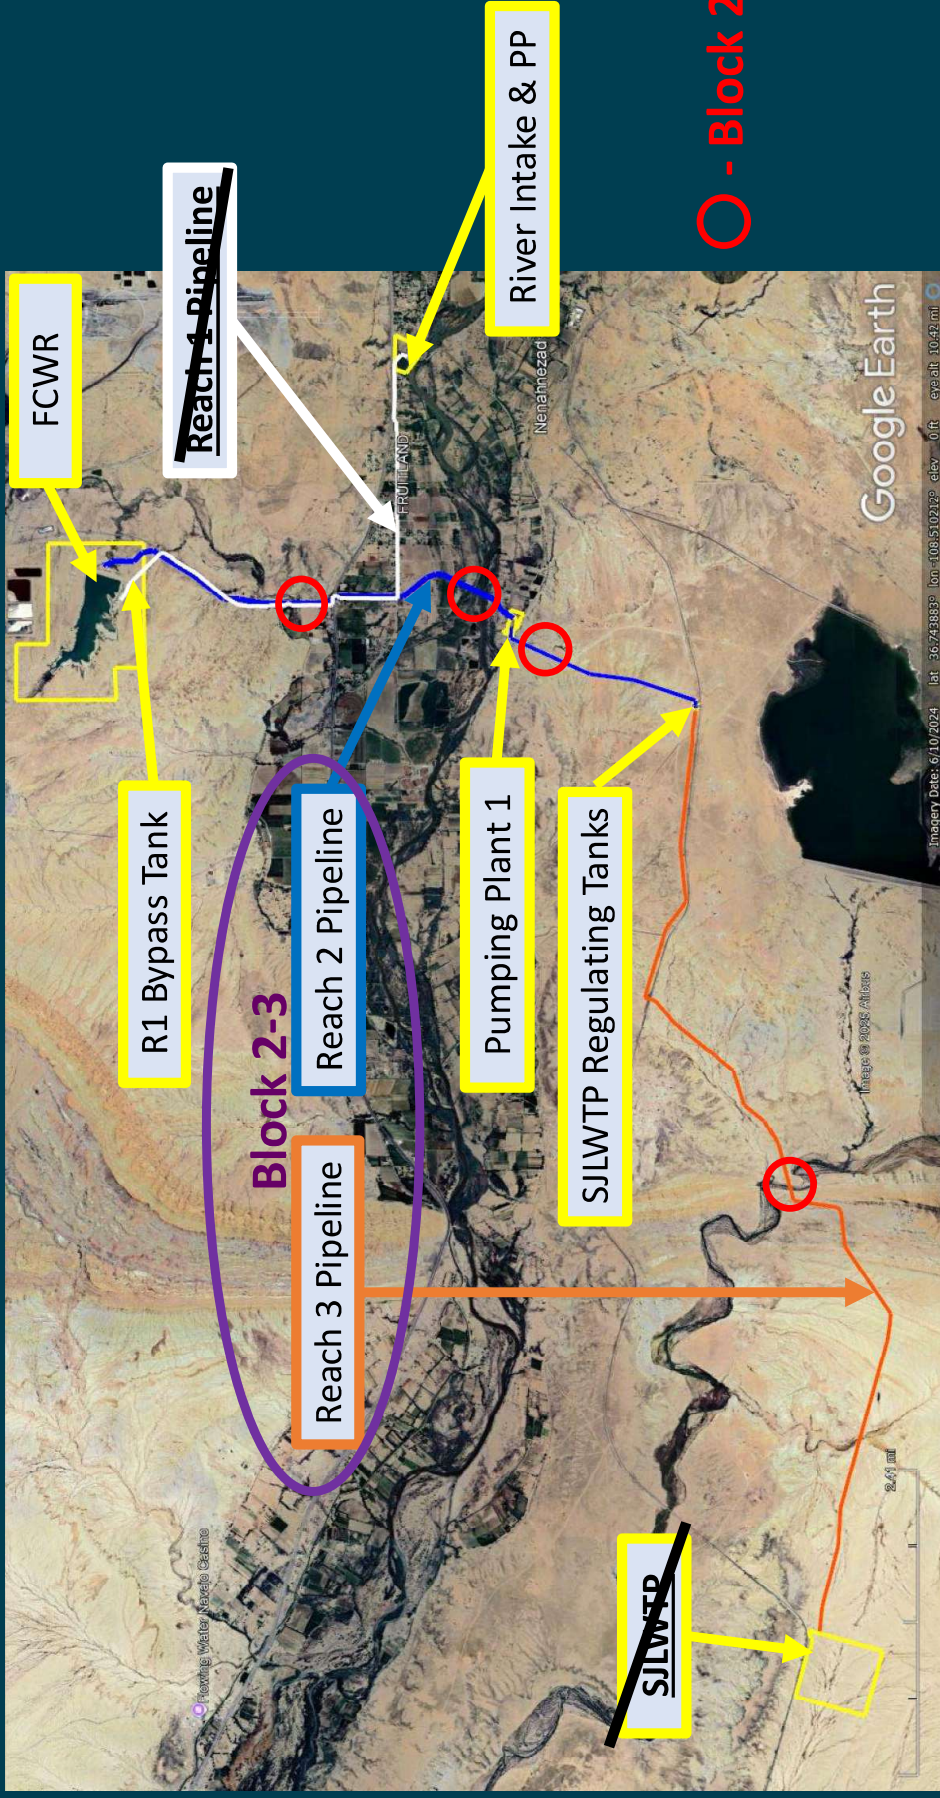


SJL Intake & River Pumping Plant

- Metal Building ~7,300 SQFT
- Four (4) 900-HP Vertical Turbine Pumps
 - Q = 71 CFS and TDH = 325 feet
- 3 Air Chambers
- Settling Channel Improvements
- Sitework & Cutoff Wall
- Steel Manifold Piping
- Electrical and SCADA Systems
- Water Quality Monitoring Equipment

Solicitation: 9/25 Award: 3/26 Construction: 6/26



SJL Intake & River Pumping Plant

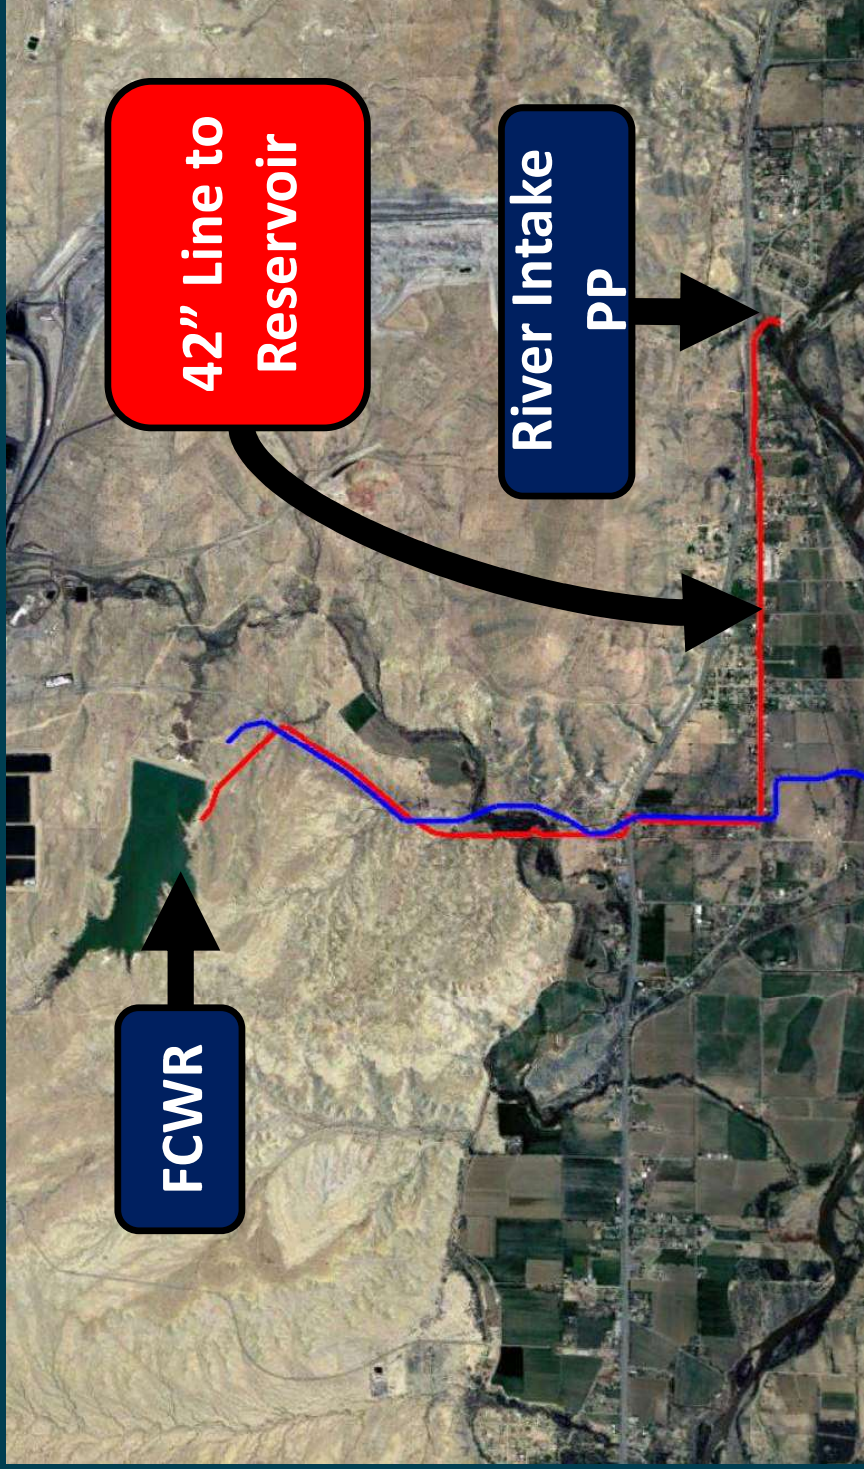


SJL Intake & River Pumping Plant




Solicitation: 9/25 Award: 3/26 Construction: 6/26



SJL Intake & River Pumping Plant

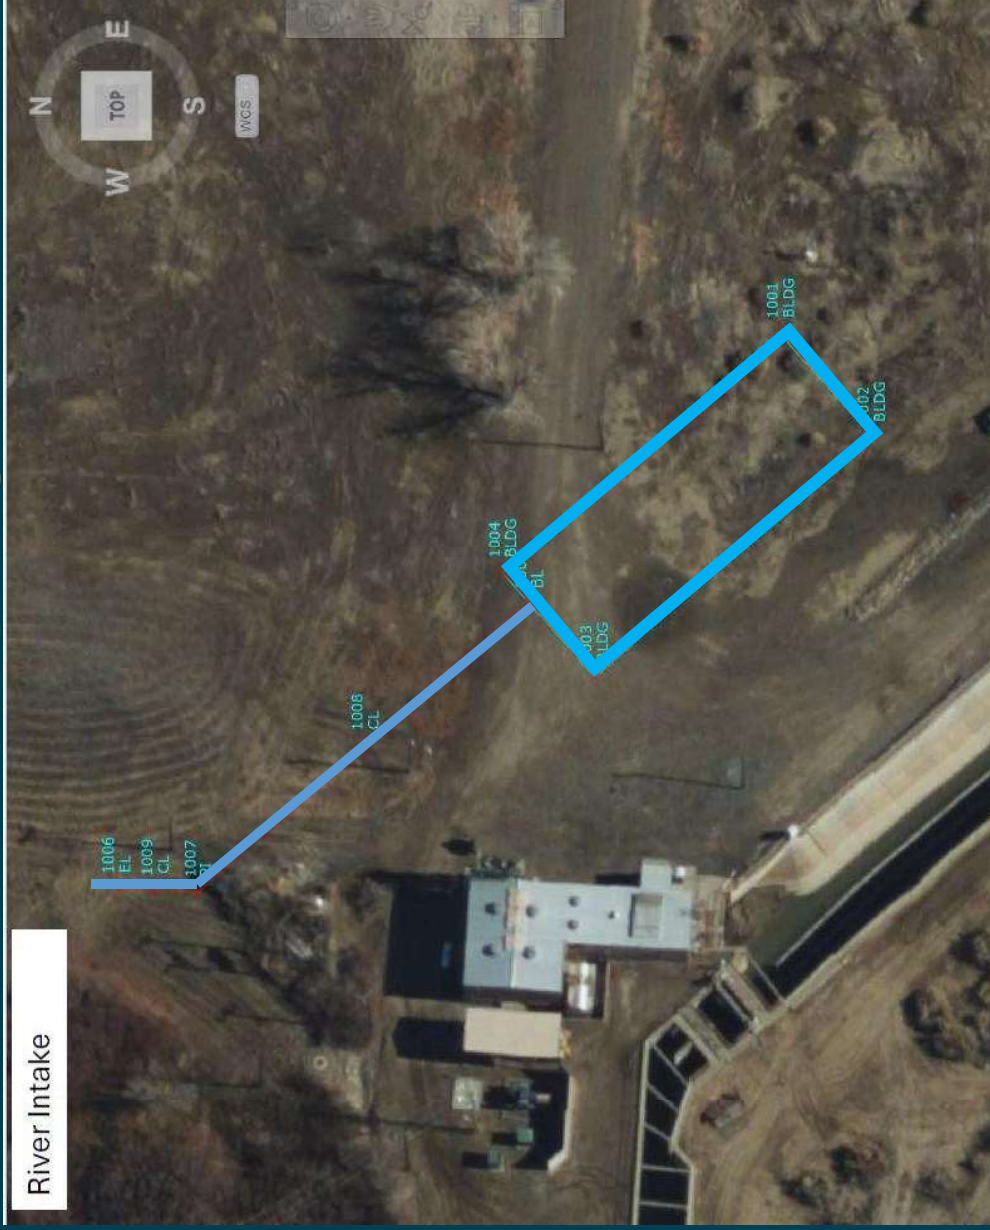


SJL Intake & River Pumping Plant

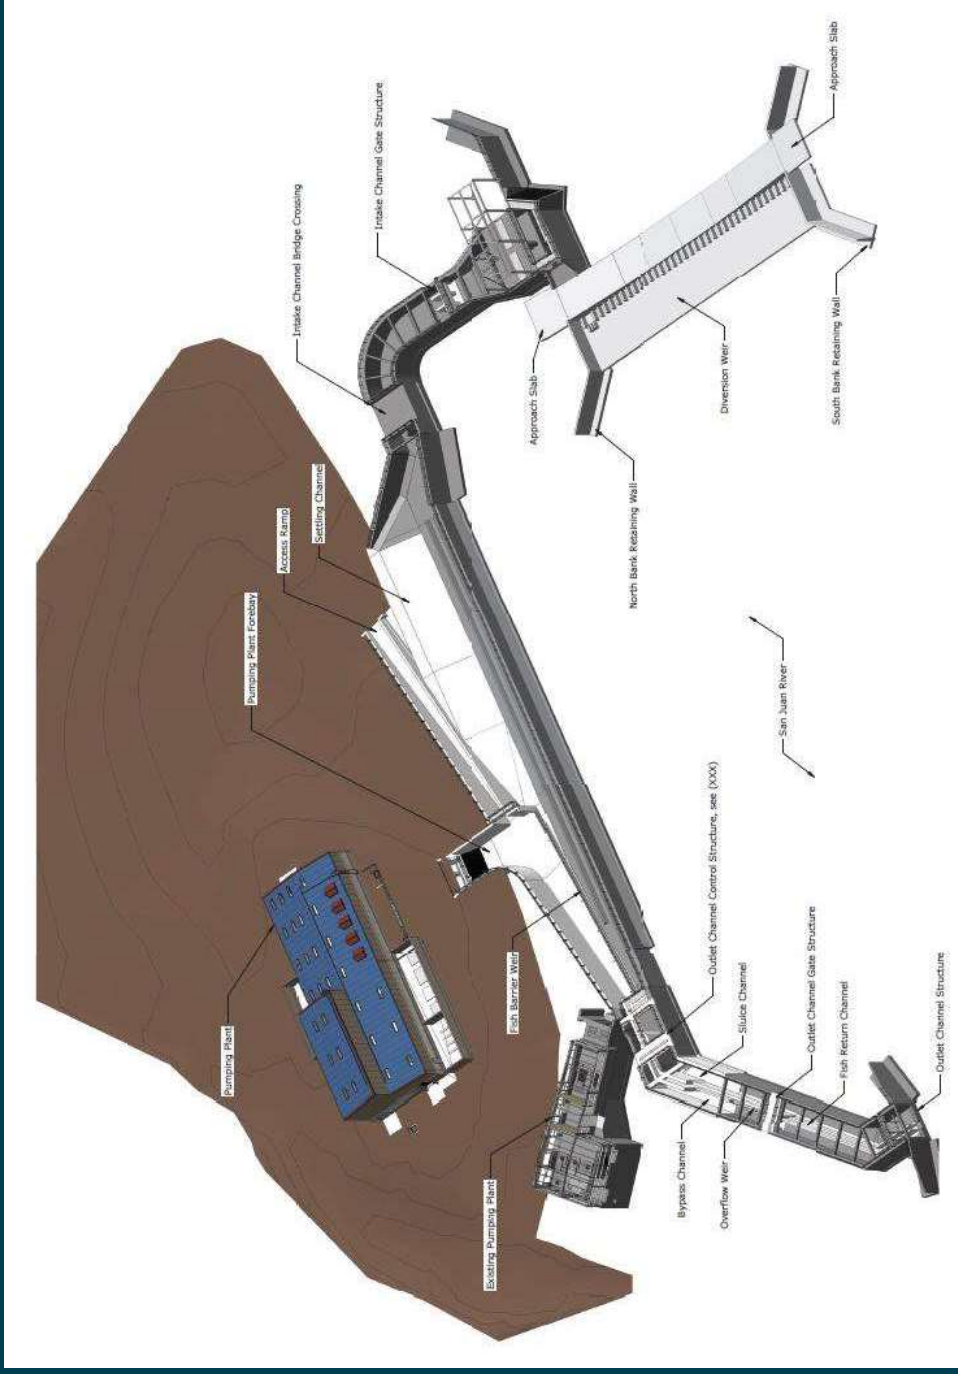


Solicitation: 9/25 Award: 3/26 Construction: 6/26

SJL Intake & River Pumping Plant

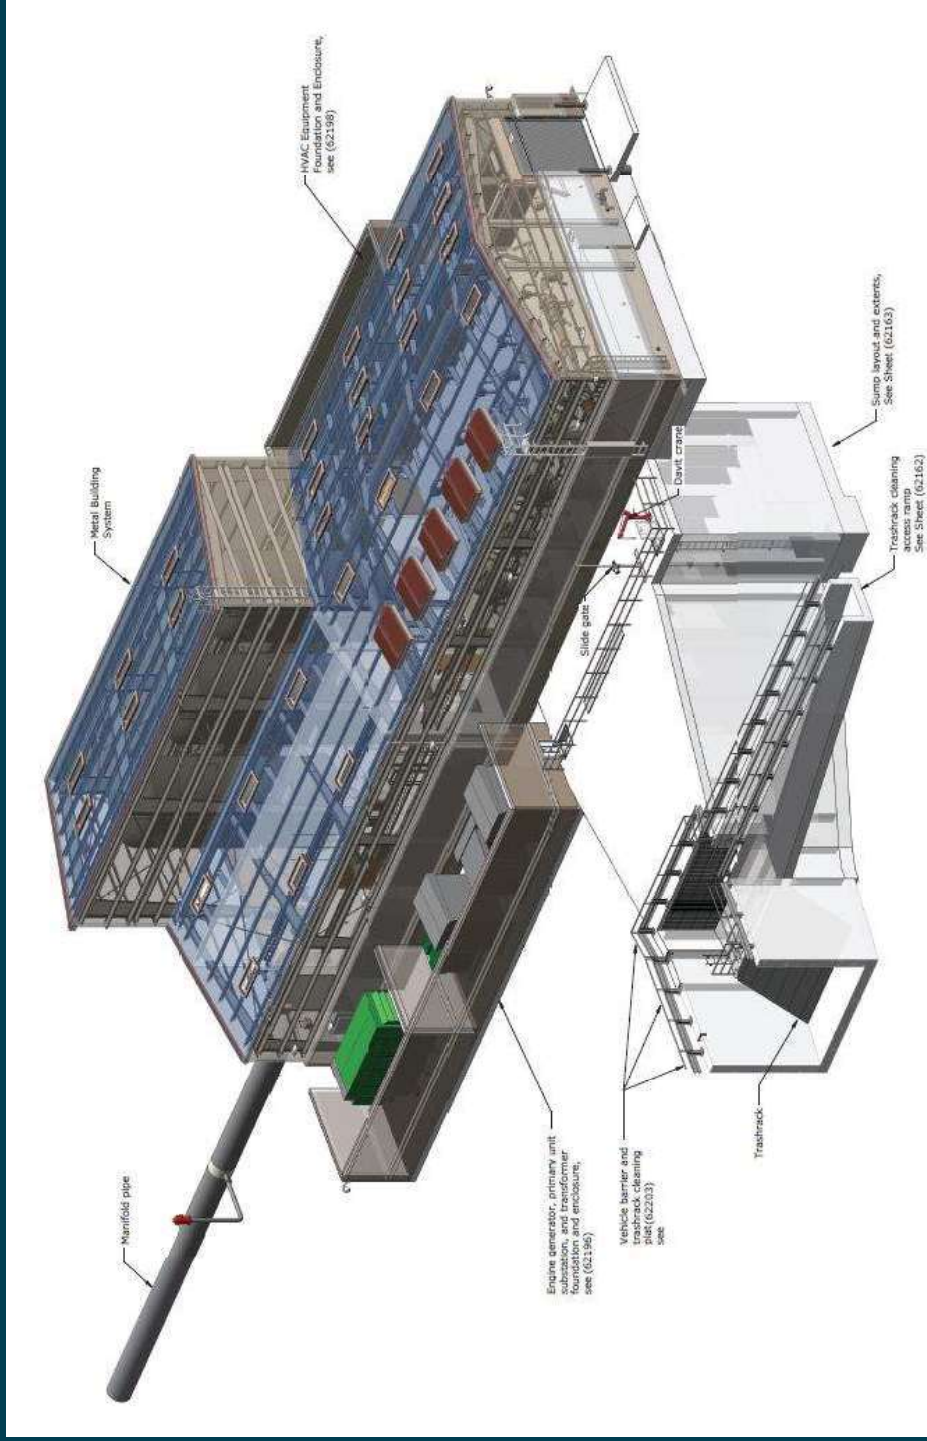

Solicitation: 9/25 Award: 3/26 Construction: 6/26

SJL Intake & River Pumping Plant

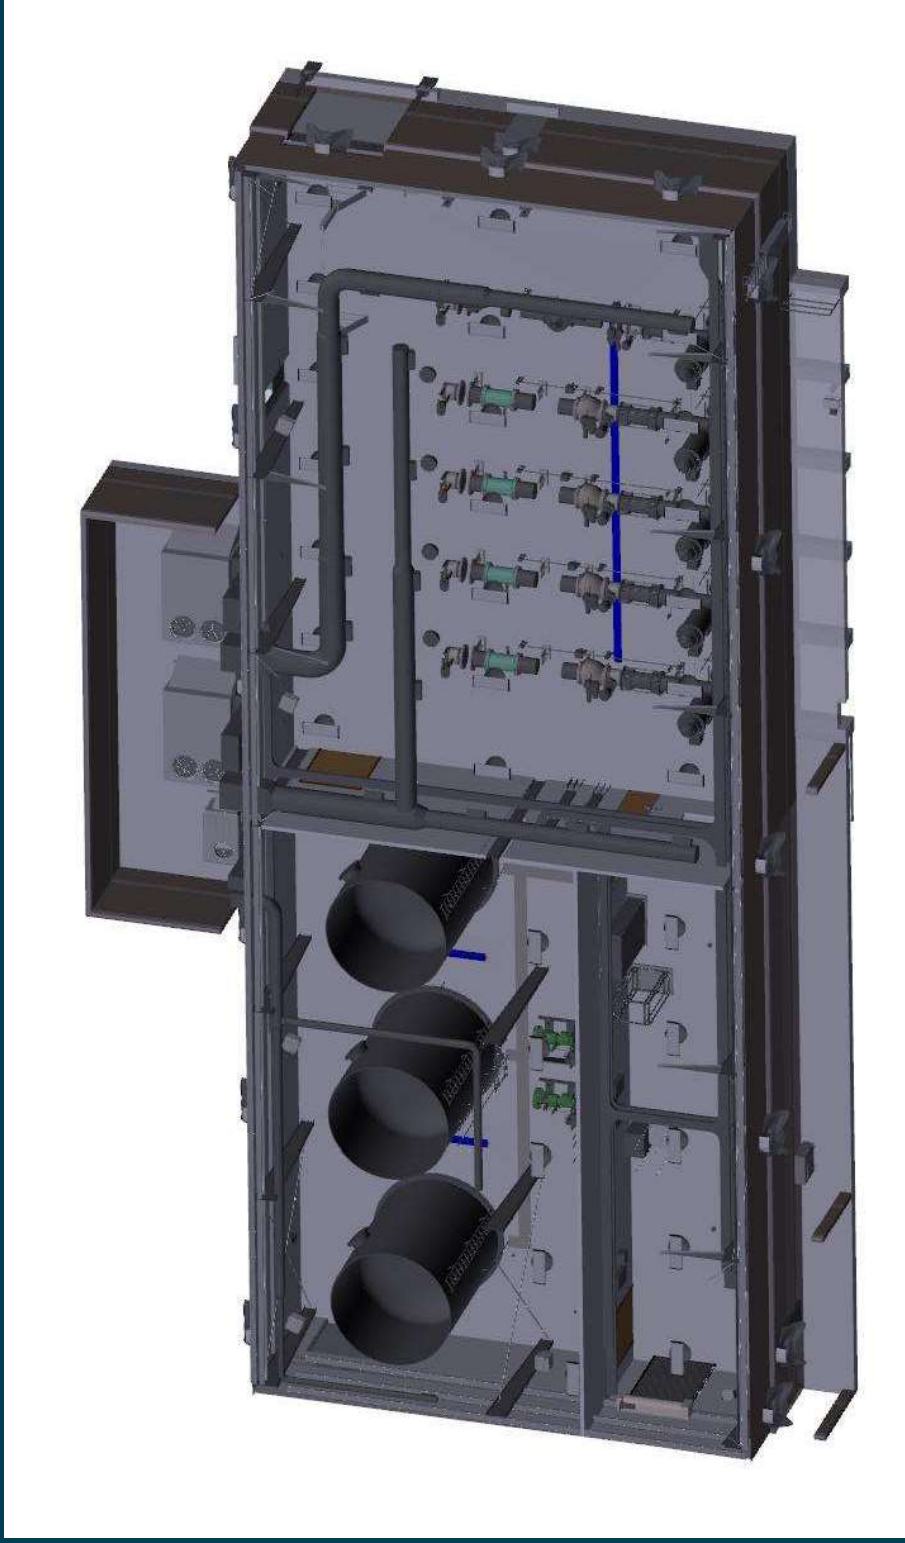

Solicitation: 9/25 Award: 3/26 Construction: 6/26




Reach 1 Bypass Tank – Not Fully Scoped Yet

- 1 MG Storage Tank – Welded Steel
- Delivery Pipeline from Reach 1
- Buried Pipeline to PNM Pumping Plant ~1,250'
- Access Road Improvements ~2,000' plus
- Power
- Cathodic Protection
- Site Grading
- SCADA
- Potentially Sediments Management

Solicitation: 5/26 Award: 9/26 Construction: 11/26



Reach 1 Bypass Tank

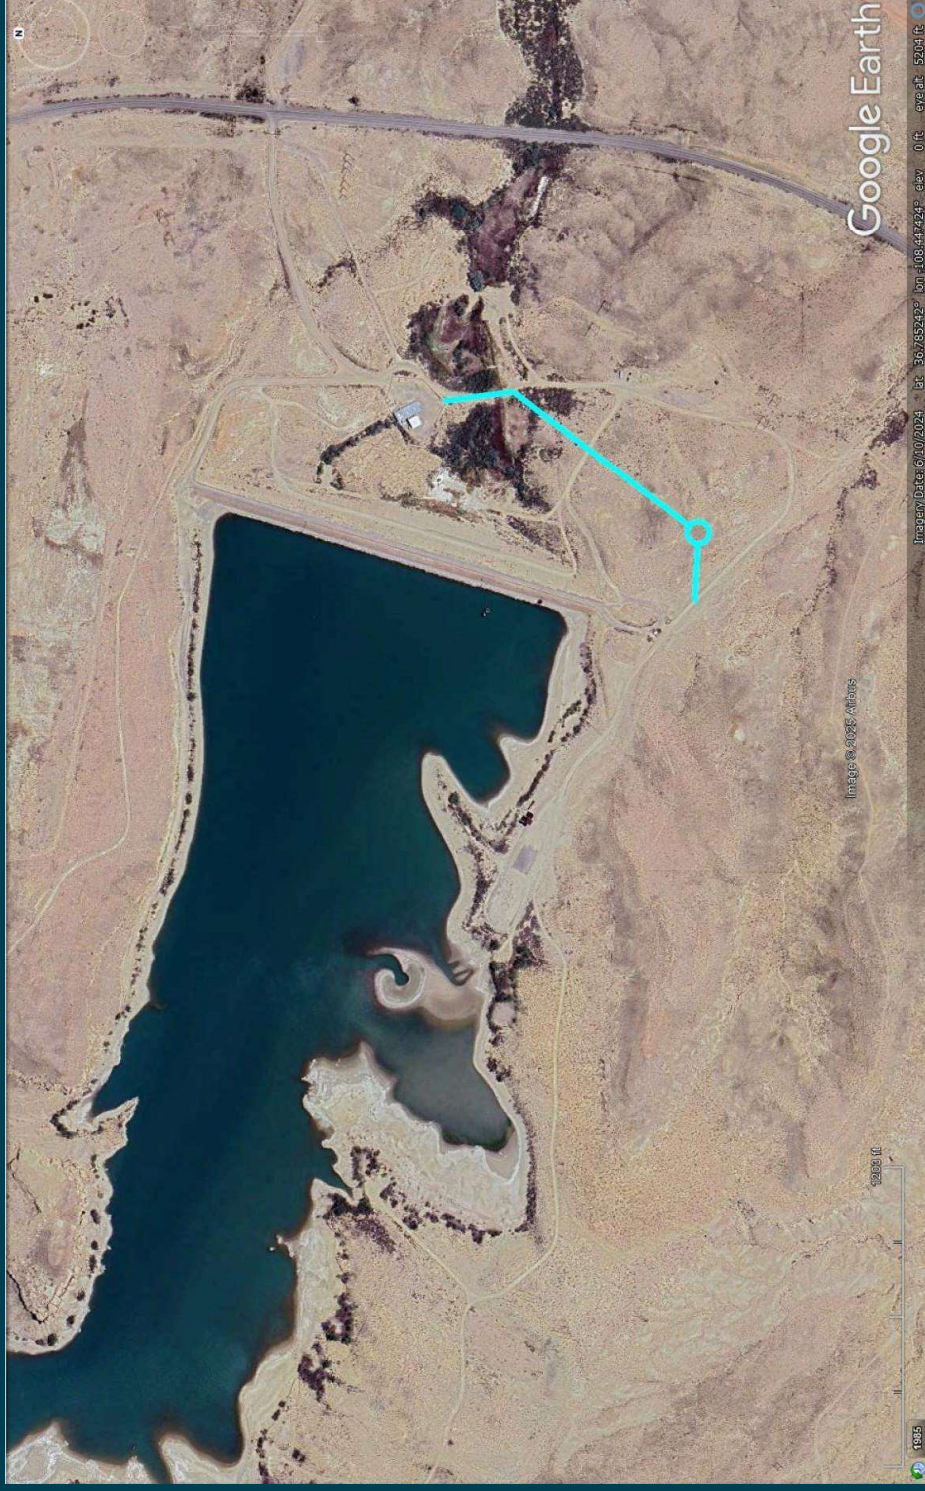

Solicitation: 5/26 Award: 9/26 Construction: 11/26



FCW Reservoir & Dam – Not Fully Scoped Yet

- Raising Concrete Sill
- Fencing
- Dam Crest Regrading
- Boat Ramp
- Riprap on Left Abutment Dam
- Pipe Tie-In Vault
- Outlet Works Improvements
 - Re-line Existing Outlet Works Outfall Pipes
 - Replace two 36"x36" slide gates, stems, and actuators
- Morning Glory Emergency Spillway Gate -- Abandon or Replace

Solicitation: 5/27 Award: 9/27 Construction: 11/27



FCW Reservoir & Dam



Solicitation: 5/27 Award: 9/27 Construction: 11/27






Block 2-3 Pipeline

- 36" to 48" Pipeline ~12 miles
- Pipeline Appurtenances
- Jack and Bore Crossings
- Two (2) - 240,000-Gallon Raw Water Concrete Storage Tanks
- SCADA
- Cathodic Protection

Solicitation: 4/26 Award: 8/26 Construction: 9/26



Block 2-3 Pipeline

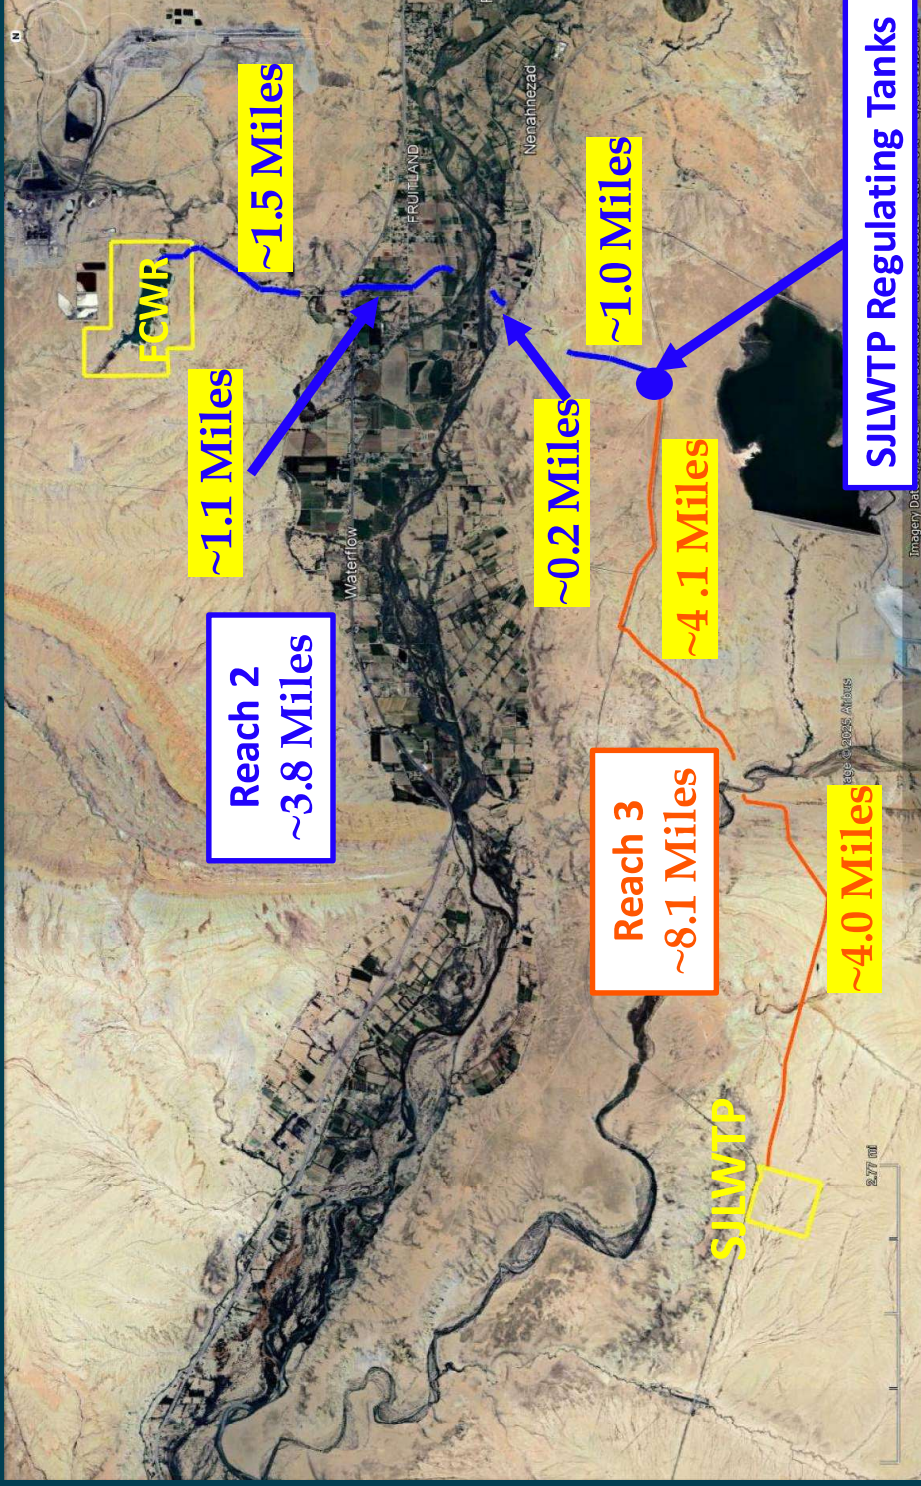


Block 2-3 Horizontal Directional Drilling

HDD CROSSINGS						
Item #	HDD Crossing Name	Length (feet)	Elevation Difference (feet)	Pipe Diameter (inch)	Reamed Diameter (inch)	Pipe Material
1	Reach 2 -- San Juan River	2,100	65	36	48	Steel
2	Reach 2 -- Nenahnezad Bluff	3,300	241	42	54	Steel
3	Reach 2 Shumway Wash	2,000	23	36	48	HDPE
4	Reach 3 -- Chaco Wash	2,000	3	36	48	HDPE

Solicitation: 1/26 Award: 6/26 Construction: 9/26




Block 2-3 Horizontal Directional Drilling

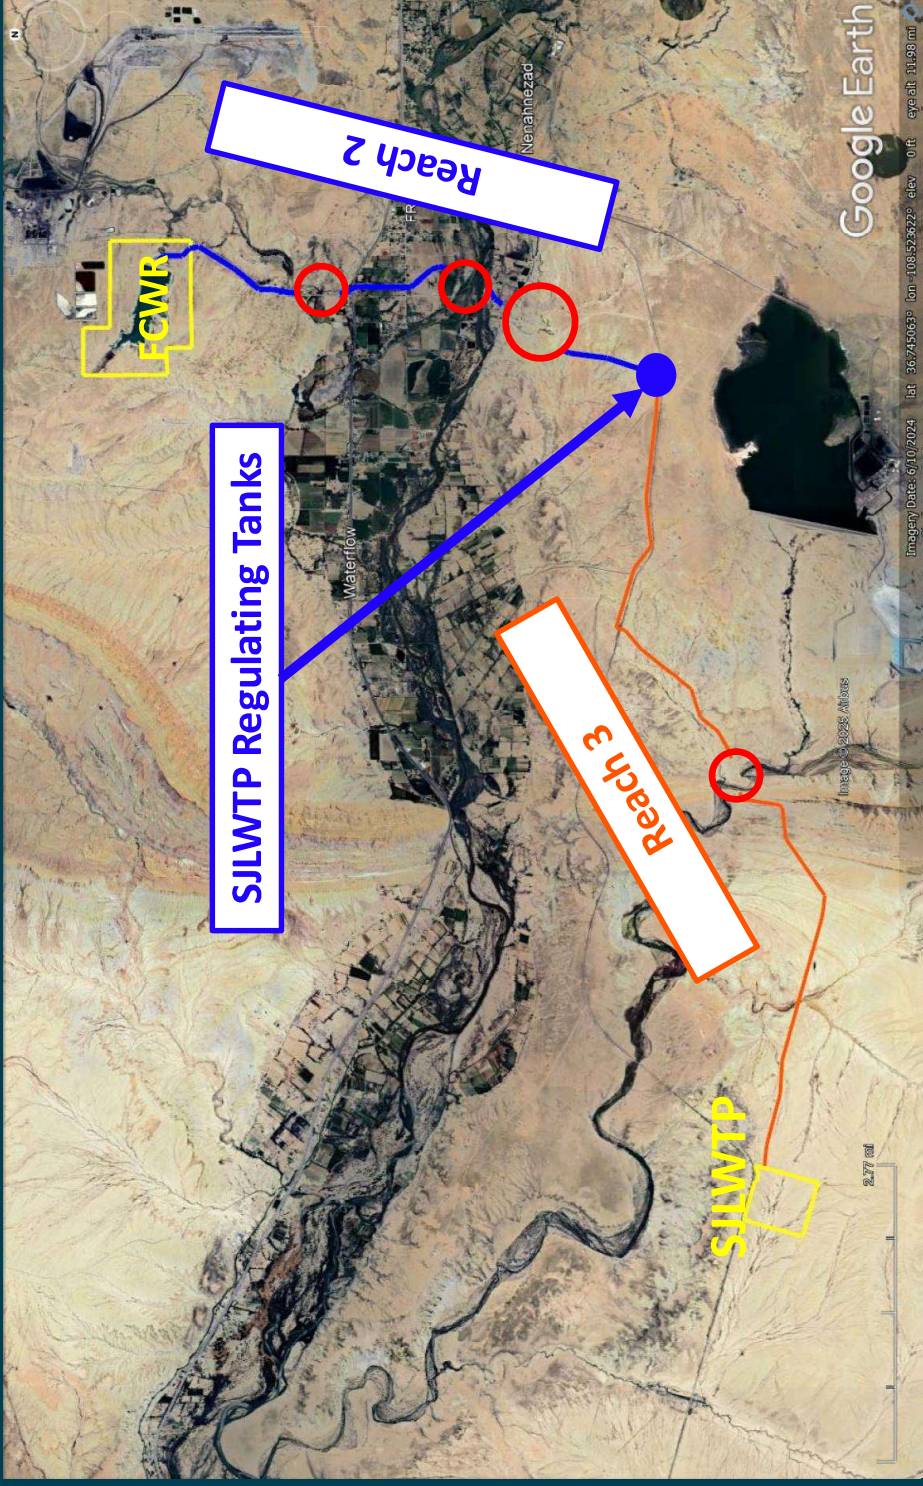


○ - Block 2-3 HDD



Block 2-3 Horizontal Directional Drilling

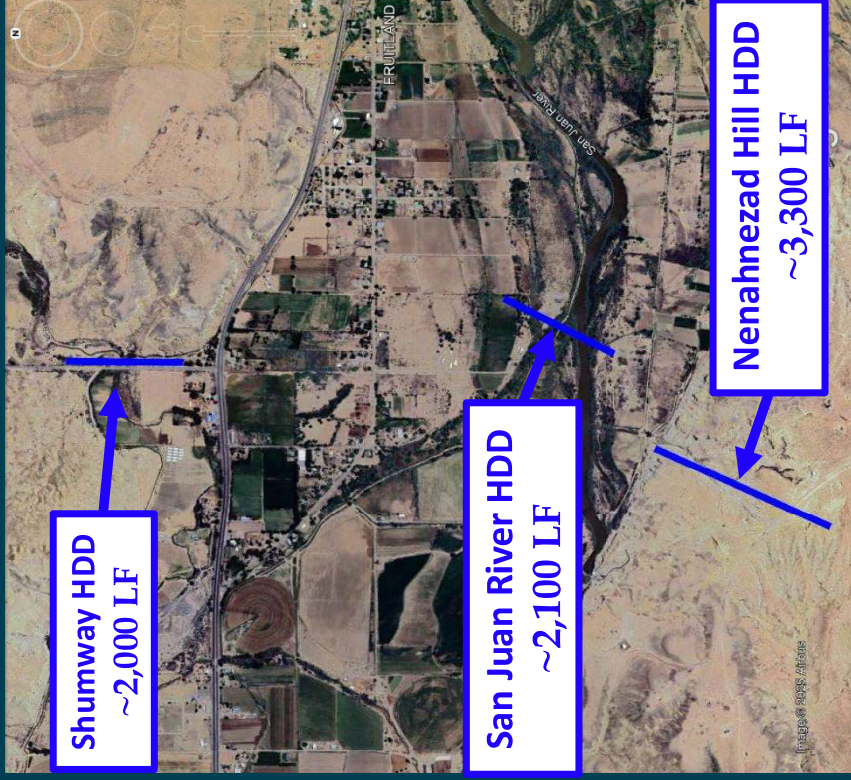

Reach 2 HDD

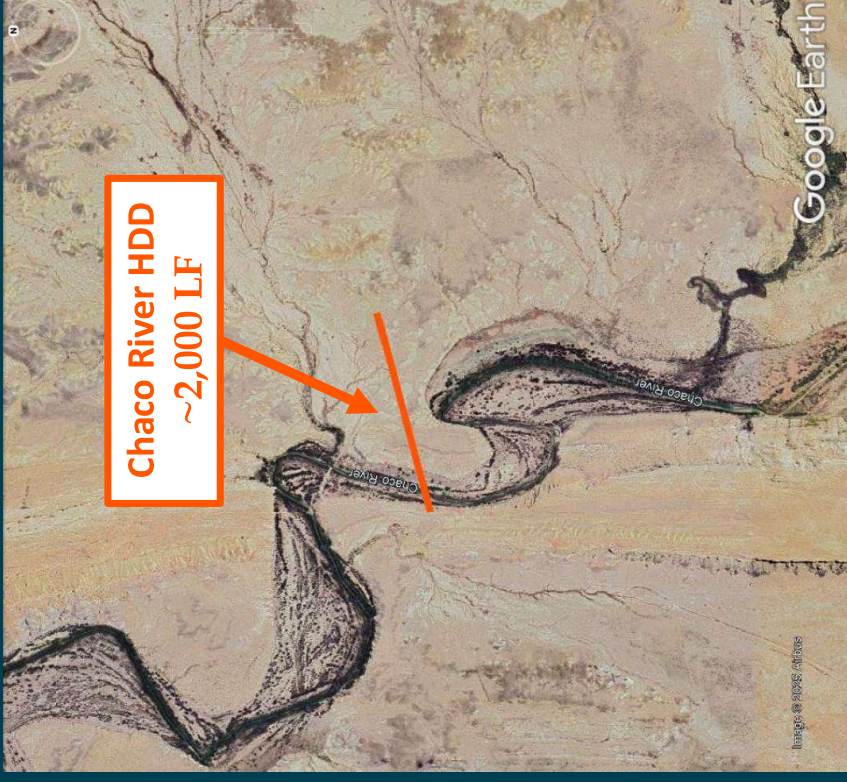

Reach 3 HDD




Pumping Plant 1

- Metal Building ~13,000 SQFT
- Six (6) 700-horsepower Vertical Turbine Pumps
 - Q = 71 CFS and TDH = 315 Feet
- Steel Manifold Piping
- 4 Air Chambers (2-2)
- Electrical System
- Precast Concrete Manholes & Vaults
- SCADA System
- Access Road improvements

Solicitation: 6/25 Award: 11/25 Construction: 2/26




Pumping Plant 1

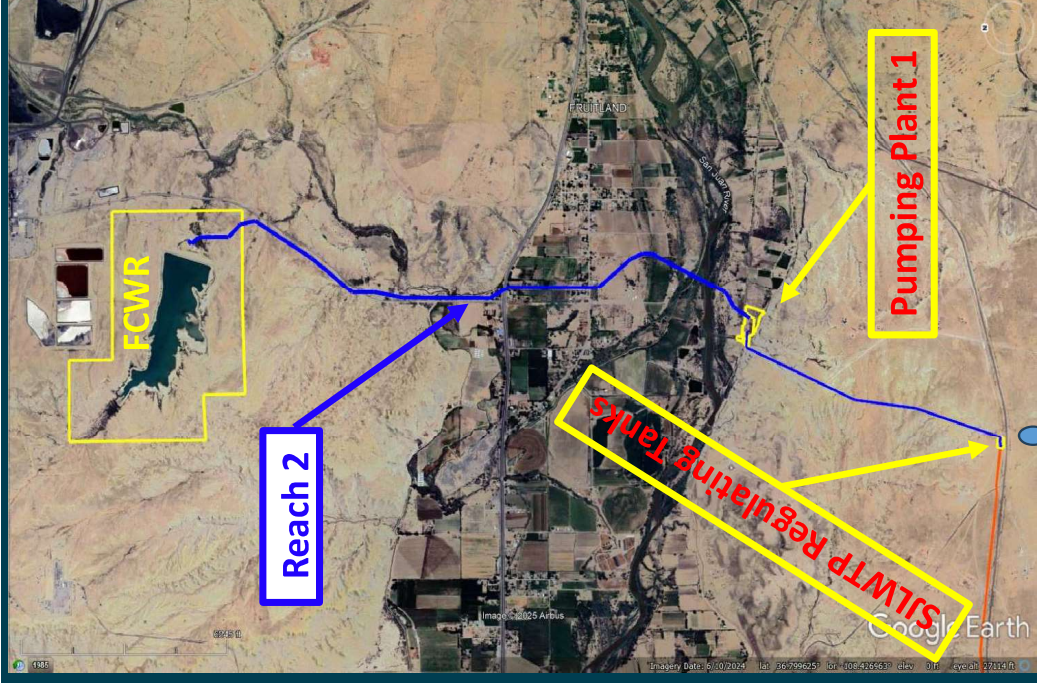

Solicitation: 6/25 Award: 11/25 Construction: 2/26

Pumping Plant 1

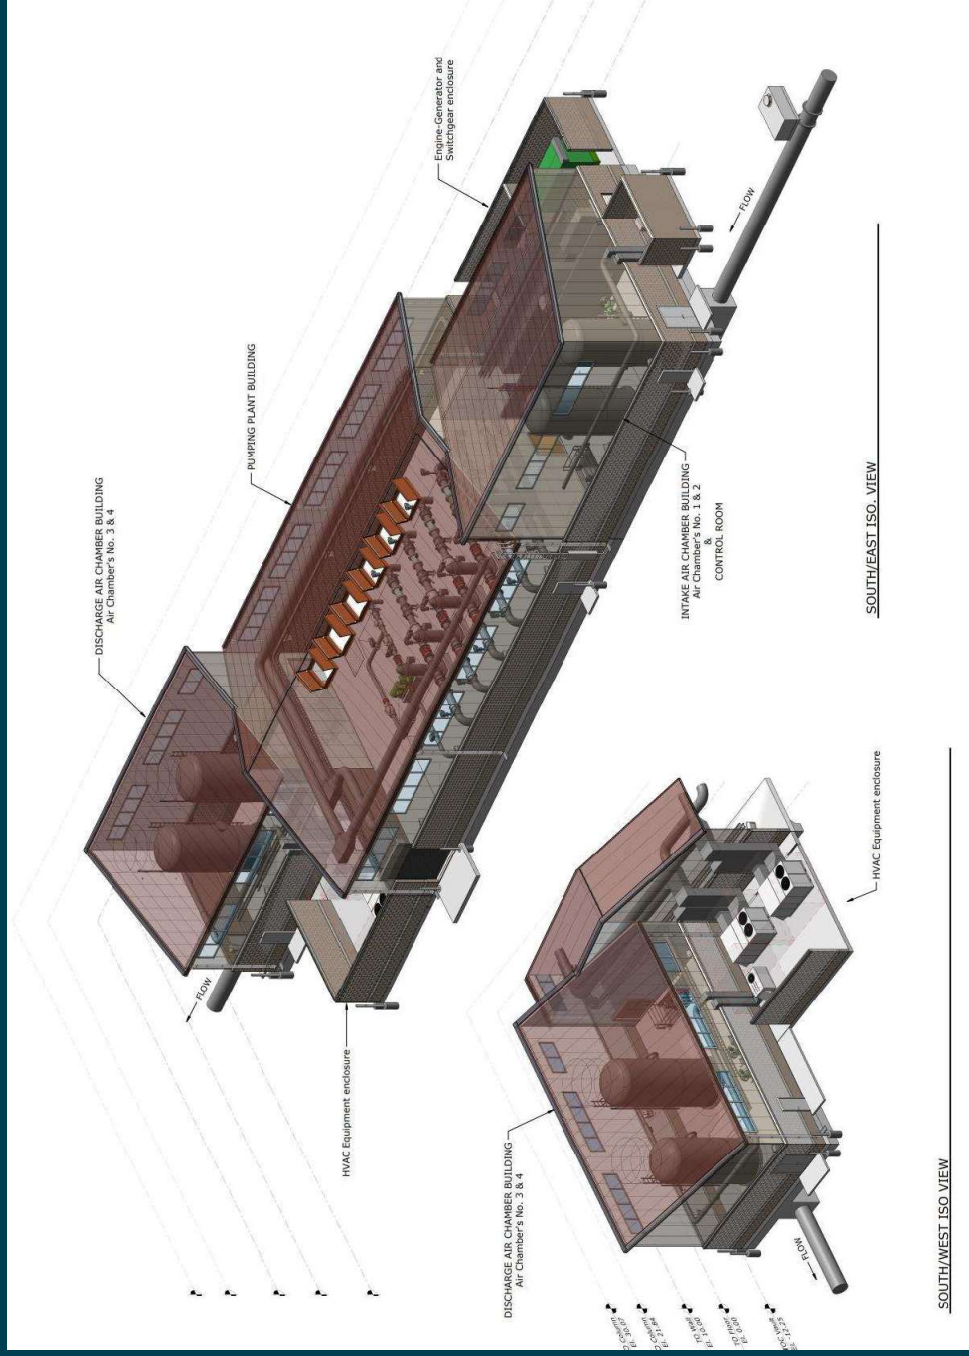

Solicitation: 6/25 Award: 11/25 Construction: 2/26


Shiprock Connection

- Pipeline ~ 6 Miles
- Pipeline Appurtenances
- Cathodic Protection
- SCADA
- Possibly Turnout Building

Solicitation: 10/27 Award: 3/28 Construction: 4/28



Shiprock Connection

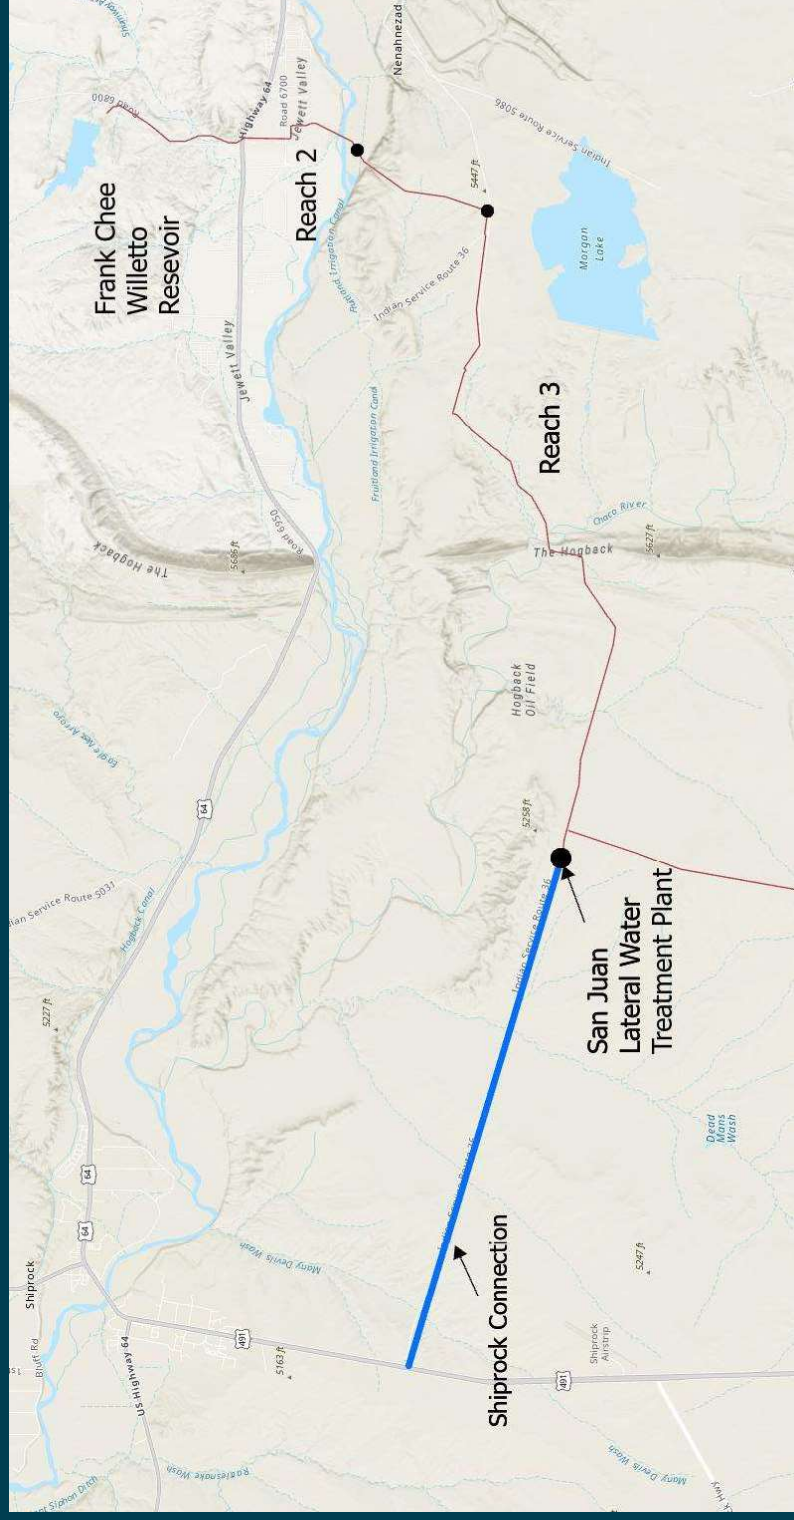

Solicitation: 10/27 Award: 3/28 Construction: 4/28



Turnout Buildings – Not Fully Scoped Yet


- 9 Connection Points Total
 - 7 along SJ Lateral
 - 2 on Code Talkers
- Access road and gravel surfacing
- Pre-cast Concrete Structure and Foundation
- Steel Manifold Piping
- Valves, Flow Meters, lighting, HVAC,
- SCADA and Power

Solicitation: 6/27 Award: 10/27 Construction: 12/27



Turnout Buildings


Item #	Reach #	Turnout Building Name	Status
1	3	Shiprock Turnout	To be designed and constructed
2	4C	Sanostee	To be designed and constructed
3	6	Newcomb	To be designed and constructed
4	7	Sheep Springs North	Already built inside PP4
5	8	Naschitti	To be designed and constructed
6	9	Crownpoint (BBN9 R10.1)	To be designed and constructed
7	10	Coyote Canyon	To be designed and constructed
8	40	Tohatchi	Already built inside PP7
9	42	Twin Lakes	Already built inside Tohlokai PP
10	12.1	Rock Springs	To be designed and constructed
11	12.2	Window Rock	To be designed and constructed
12	13	City of Gallup Regional	To be designed and constructed

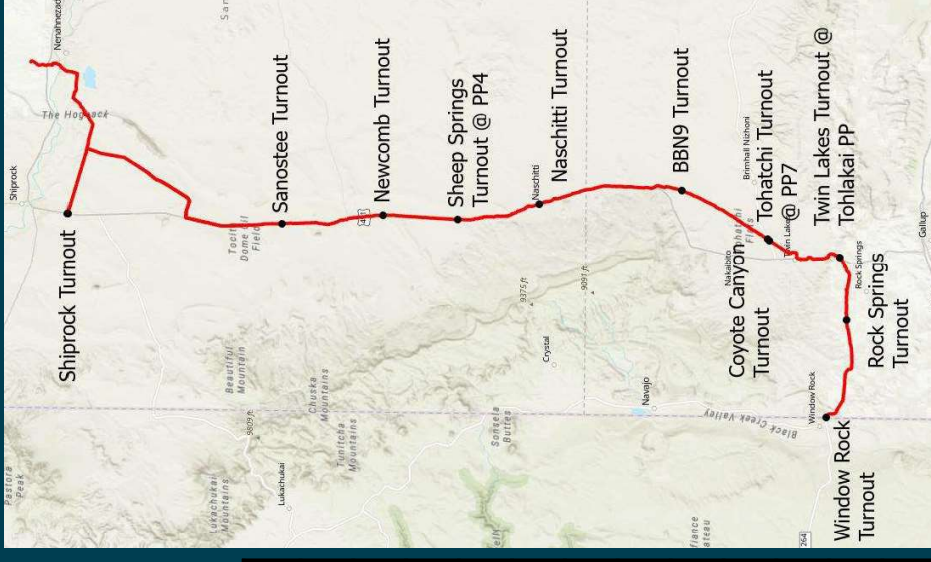

Solicitation: 6/27 Award: 10/27 Construction: 12/27

Reach 14.6a, 14.7a, 14.8a

- Pipeline 8" to 14" HDPE ~ 8 miles
- 2 Booster Pumping Stations
- 650,000-Gallon Water Storage Tank
- SCADA & Communication Line

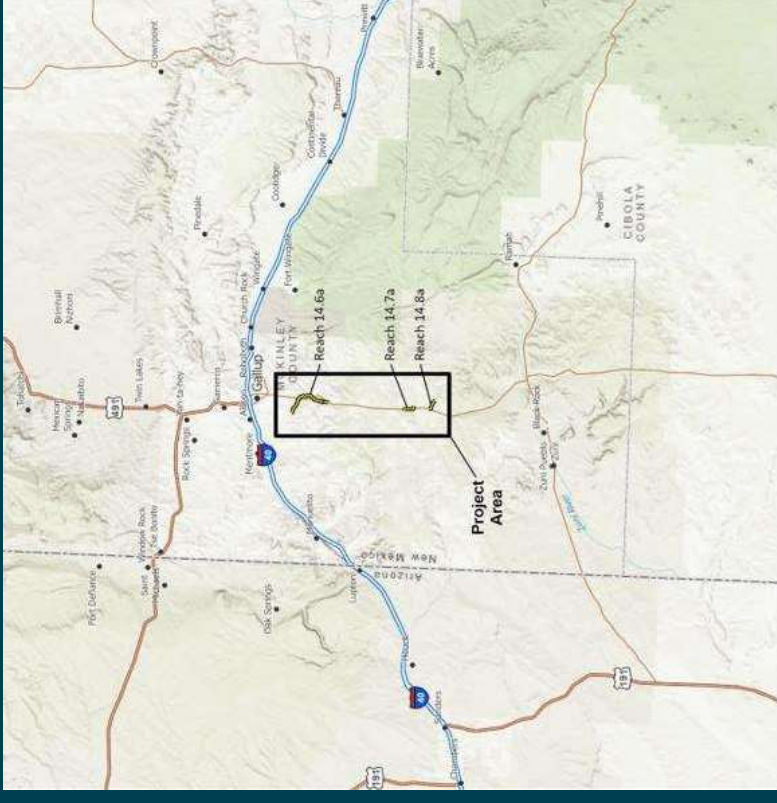

Solicitation: 2/28 Award: 6/28 Construction: 8/28



DZ Booster / Pumping Plant / Site 3 Tank

- Access Road
- Concrete Foundation
- Pre-Engineered Booster Pump Station
- 500,000-Gallon Steel Tank
- Site Grading and Erosion Prevention
- Steel Manifold Piping
- Fencing
- Power and SCADA

Solicitation: 9/25 Award: 1/26 Construction: 3/26



DZ Booster / Pumping Plant / Site 3 Tank

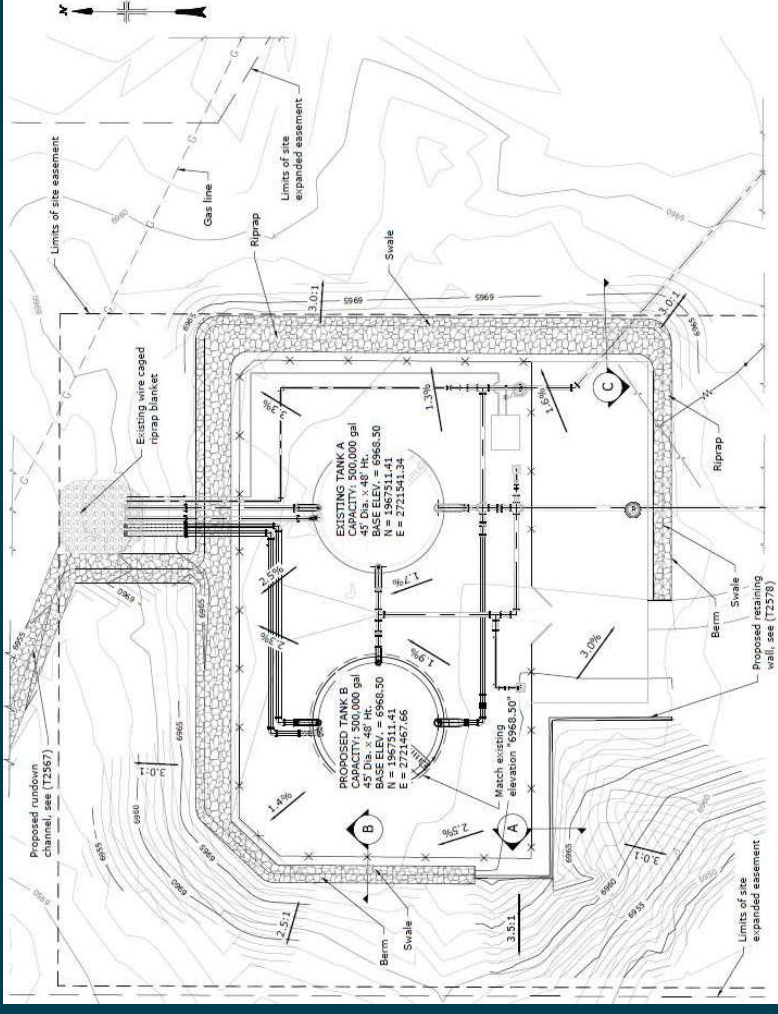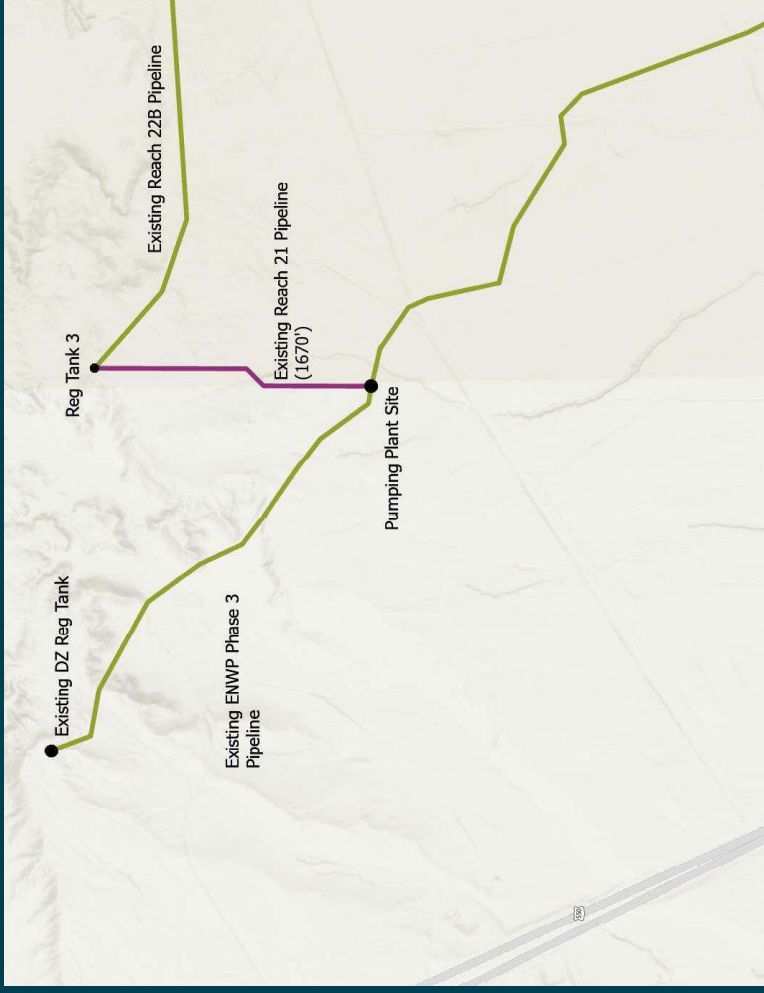


Solicitation: 9/25 Award: 1/26 Construction: 3/26

Project Timeline

REMAINING NGWSP PROJECTS					
Item #	Project	Solicitation	Award	Start of Construction	End of Construction
1	SJL Intake & River Pumping Plant	September 25, 2025	March 20, 2026	June 5, 2026	October 6, 2028
2	Reach 1 Bypass Tank	May 7, 2026	September 10, 2026	November 1, 2026	September 1, 2027
3	FCW Reservoir & Dam	May 10, 2027	September 13, 2027	November 1, 2027	May 1, 2028
4	Block 2-3 Pipeline	April 10, 2026	September 16, 2026	November 4, 2026	August 11, 2028
5	Block 2-3 HDD	October 29, 2025	April 22, 2026	June 10, 2026	August 24, 2027
6	Pumping Plant 1	June 24, 2025	November 11, 2025	January 27, 2026	May 30, 2028
7	Shiprock Connection	October 14, 2027	March 2, 2028	April 20, 2028	March 1, 2029
8	Turnout Buildings	June 5, 2027	October 23, 2027	December 11, 2027	August 25, 2028
9	Reach 14.6a, 14.7a, 14.8a Pipeline	February 11, 2028	June 30, 2028	August 18, 2028	June 29, 2029
10	DZ Booster / Tank	December 1, 2025	April 6, 2026	May 25, 2026	April 8, 2027



Acquisition Plan (Contracting)

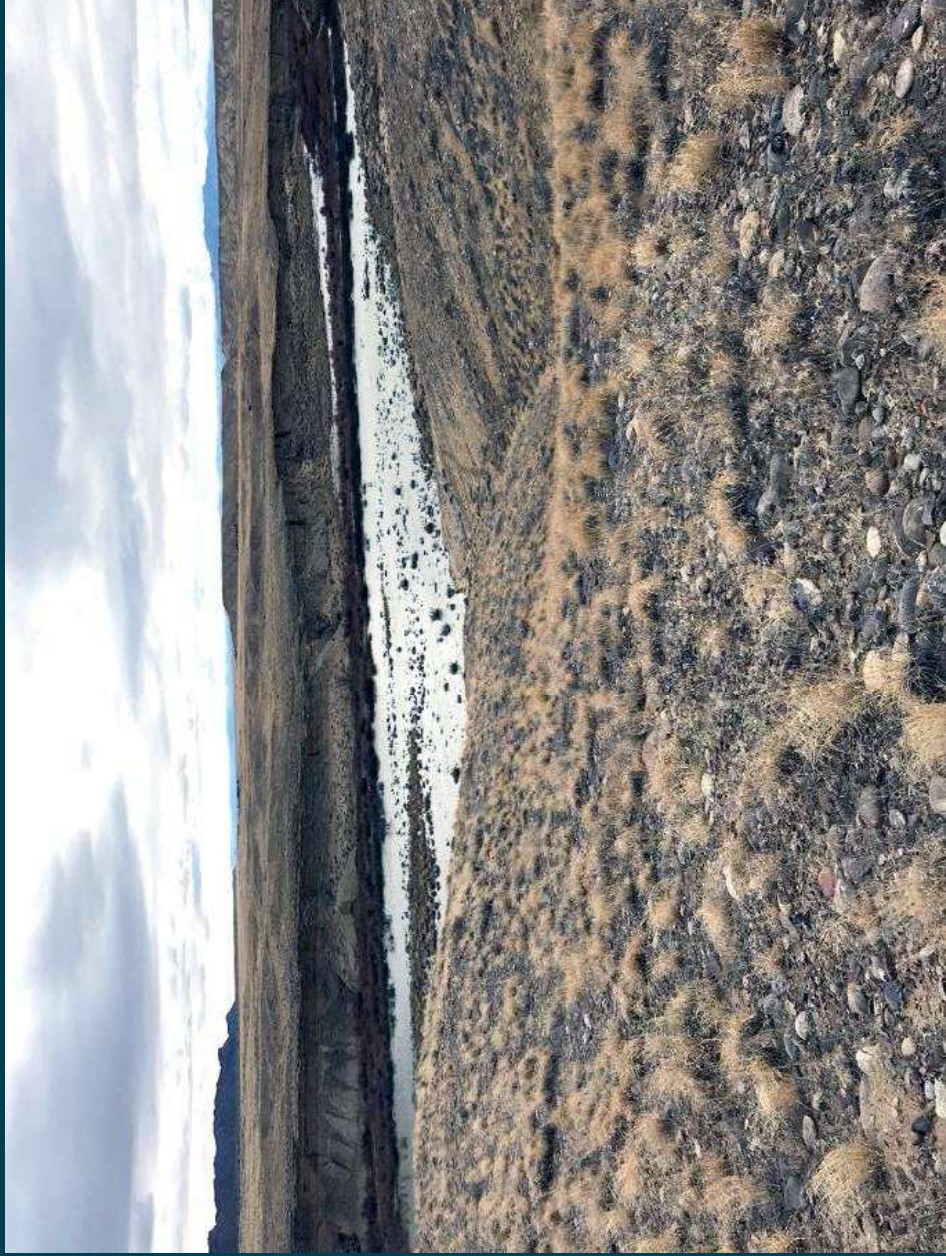

Purpose of Industry Day

- Looking for capable firms to help Reclamation meet its construction needs (Small & Large businesses)
 - Open to suggestions that would make firms more interested in Reclamation projects
 - Cannot waive requirements we don't have the authority to waive (e.g. payment terms, contract type, etc.)
- Reclamation relies on construction contractors to meet its responsibilities
 - Please submit any suggestions or criticisms of the contract process to Amy Loveless @ aloveless@usbr.gov and Ashton Jones @ ajones@usbr.gov and we will review the suggestions to see if the process can be improved to gain more interest in our requirements



Solicitation Process

- FAR 15, Firm-Fixed Price (FFP)
 - Best Value Tradeoffs, most likely technical equal to price
 - Common evaluation factors: Technical Approach, Safety, Past Performance
 - SB Set-aside projects are likely to be more streamlined and easier to respond to compared to the estimated \$35M+ full and open requirements.
 - Lower page limitations on responses
 - Less stringent on Sections L&M



Set-Aside vs. Full-and-Open Competition

- Based on estimated values and NGWSP historical data.
- Possibly set-aside for small business:
 - DZ Booster/Tank
 - Reach 1 Bypass Tank
 - Turnout Buildings
 - FCW Reservoir & Dam
 - Shiprock Connection
 - Reach 14.6a, 14.7a, 14.8a Pipeline
- Most likely full-and-open competition:
 - Pumping Plant 1
 - SJL Intake & River Pumping Plant – Reach 1
 - Block 2-3 HDD
 - Block 2-3 Pipeline



Indian Preference Clauses

- Give preference to directly hiring Indians who can perform the work required
- Give preference to Indian organizations & Indian-owned economic enterprises for subcontracts.
- Provide opportunities for training to include on-the-job, classroom or apprenticeship.
- Establish an Indian preference program:
 - Liaison Officer
 - Advertisement of jobs/subcontracts
 - Subcontracting program with preference
 - Maintain written records



Usual Contracting Process

- Issue Small Business Sources Sought – Issued on SAM.gov to get interest from SB's to include capabilities statement, bonding level, etc.
- Synopsis – Issued on SAM.gov at least 30 days before solicitation. This is required by the FAR and may include a copy of the DRAFT solicitation, Specifications, Drawings, etc.
- Solicitation – Issued on SAM.gov. Usually, open 60-90 days depending on the requirement.
- Site Visit – Usually about a week after solicitation is issued.
- Solicitation Clarification Questions – Usually due about one to two weeks after Site Visit.
- Solicitation Amendments – Issued on SAM.gov to provide clarification questions and BOR answers. Will possibly include updates to Specification and/or drawings if needed.
- Oral Presentations – Will probably be required for the larger requirements during the evaluation period. Instructions will be in Section L of each solicitation.



Tariffs

- Applicable Tariffs follow the rules of clause FAR 52.229-3 Federal, State and Local Taxes.
- Any Tariffs effective before the award is issued, should be included in your pricing.
 - If a tariff becomes effective between the time you submit your proposal and before the award is issued, contact the Contract Specialist and Contracting Officer ASAP to submit updated pricing to include applicable tariffs.
- Any Tariffs that become effective after the award is issued, those should be submitted through the Department of Commerce. The Contract Specialist or Contracting Officer can provide you additional information at that time.



Questions and Answers



Site Tour (12:05 pm – 4:00 pm)

• Leave College	12:15 pm
• Arrive at Frank Chee Willetto Reservoir	12:45 pm
• Leave Frank Chee Willetto Reservoir	1:15 pm
• Arrive at River Intake Pumping Plant	1:25 pm
• Leave River Intake Pumping Plant	1:55 pm
• Arrive at Pumping Plant 1	2:10 pm
• Leave Pumping Plant 1	2:40 pm
• Arrive Nenahnezad Horizontal Directional Drill	2:45 pm
• Leave Nenahnezad	3:00 pm
• Arrive at SJLWTP/Shiprock Turnout	3:20 pm
• End of Tour	4:00 pm



JOB HAZARD ANALYSIS
Industry Day Tour
Date: April 2, 2025

JHA Review and Signatures:

REVIEWS AND SIGNATURES			
JHA Created By:		Reviewed by:	
Name		Name	
Emma Mancaneres 505-427-684		Bart Deming 505-436-4932	
Hilda Castillo Smith 505-238-4558	Digitally signed by HILDA CASTILLO SMITH DN: cn=HILDA CASTILLO SMITH, o=CR 6800, ou=CR 6800	Ryan Gladden 505-793-9539	Digitally signed by RYAN GLADDEN DN: cn=RYAN GLADDEN, o=CR 6800, ou=CR 6800

Ambulance and fire departments are contacted by the following telephone numbers:

Emergency Services
San Juan County Sheriff
Navajo Nation Police
Shiprock
New Mexico State Police
San Juan Regional Medical Center
San Juan Regional Medical Center (Air Life)
911
(505) 334-6107
(505) 786-2050
(505) 325-7547
(505) 609-2000
(505) 325-5011

Operations to be performed:

- Review JHA.
 - Total tour time is approximately 4 hours.
 - Follow lead vehicle, park as directed.
 - Follow Deputy Construction Engineer directions.
- Travel from San Juan College to Frank Chee Willetto Reservoir
 - HWY 64 is a well-traveled road.
 - Be aware of traffic, animals, and construction zones
 - Walk to the site
 - Watch footing
 - Uneven terrain
 - Snakes and rodents might be present
- Travel to the River Intake Pumping Plant.
 - Heading South on County Road 6800, turning left (heading East) onto Highway 64.
 - use the furthest left/East turn lane on CR 6800
 - Walking near edges or another precipice.

- Maintain proper footing and watch where you step.
- Travel to Pumping Plant 1 and Nenahneazad Hill HDD.
 - Rd 6675/N 365
 - Narrow winding road
 - Be aware of speed
 - Access roads to site
 - East Side:
 - Residential road.
 - Be aware of dogs.
 - West Side (Nenahneazad Hill):
 - Narrow road. Stay to the right side of the road.
 - Watch out for potholes
 - Walk to the site
 - Watch footing
 - Uneven terrain
 - Snakes and rodents might be present
 - Travel to SJL Water Treatment Plant – Shiprock Turnout.
 - HWY N36 is a well-traveled road.
 - Be aware of speed
 - Walk to the site
 - Watch footing
 - Uneven terrain
 - Snakes and rodents might be present

Identified Potential Hazards and Mitigation Efforts:

Specific Hazard	Solution
Heat Exhaustion and sun exposure	Stay hydrated and wear sunscreen.
Slips, Trips, Falls	Walk carefully, wear proper footwear (no sandals or open toed shoes), avoid problem areas, if possible, allow reasonable distance from other personnel, walk slowly.
	Be aware of rodent holes.




Specific Hazard	Solution
Weather Conditions	Be prepared for the current weather conditions and be prepared for weather changes, wear rain gear if needed. Weather bug ap will be monitored by resident engineer for lightning in area. When lightning is 5 miles away, get in vehicle.
Travel Hazards	Drivers may encounter livestock, wildlife, or poor road conditions. Wear seat belt and drive defensively.

Safety Related Equipment:

1. Proper Clothing
2. High Visibility vest, if required.
3. Closed toe sturdy shoes
4. First Aid Kit located in vehicles
5. Cell Phone
 - a. If service is unavailable, send someone to a site where they can get service.





— BUREAU OF —
RECLAMATION
